

# Monitoring the 3RF Commitments

## Dashboard 3RF Monitoring Framework

### About this document


This Monitoring Framework tracks all the 3RF commitments in the 3RF document published Dec 2020. This dashboard shows at a glance the progress on commitments and their milestones.

The commitments are divided by 3RF Working Group, the leads and co-leads of which are responsible for keeping the framework up to date. The WGs are responsible for working towards the achievement of the commitments at a technical level, by setting priorities, identifying synergies, gaps and opportunities for implementation.


On each tab, the commitments are divided into track 1 (People Centered Recovery) and track 2 (Reform and Reconstruction). Commitments are also divided by type of intervention: Reforms and Policy Actions; Institutional Strengthening; and Investments and Programmes. The wording of commitments was agreed at CG-level. For each commitment, milestones can be defined by the WG, allowing the flexibility to break down commitments into manageable actions. For example, the commitment may be the passing of a certain law; the milestones may be inclusive drafting sessions, lobbying parliament, and then implementing the law.

This Monitoring Framework will be subject to review to ensure it fulfills its purpose of capturing initiatives feeding into the 3RF commitments from the main actors of each stakeholder group in each sector. This Monitoring Framework is a living document with the aim of being updated for each CG meeting.




### Progress against all 3RF Commitments

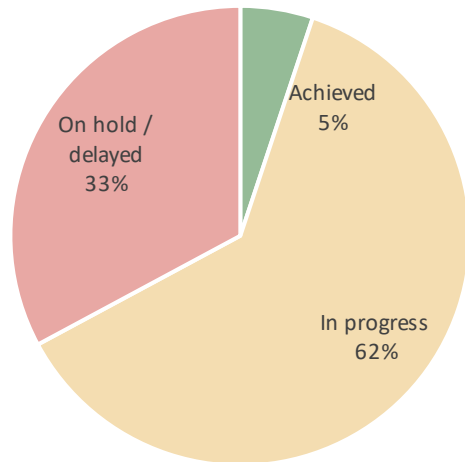

### Progress on Commitments by Pillar

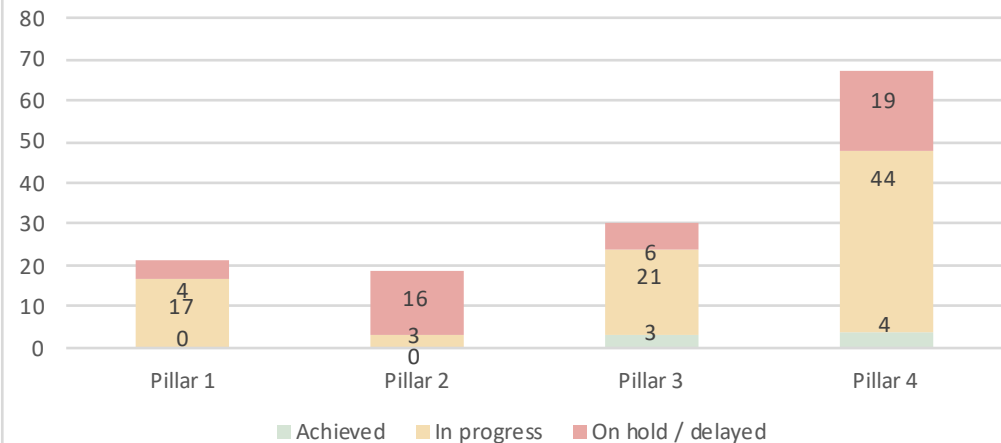

# Monitoring the 3RF Commitments

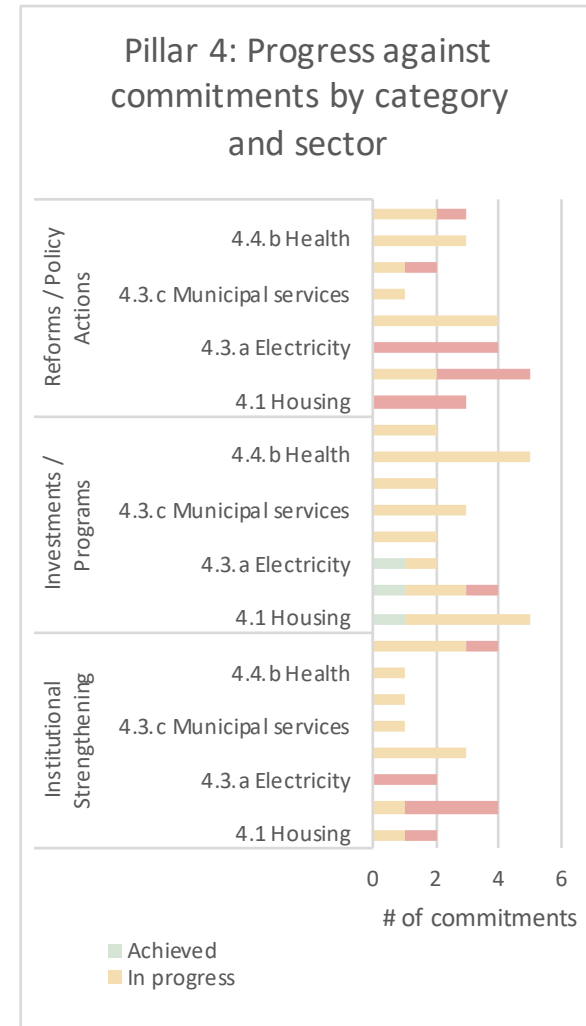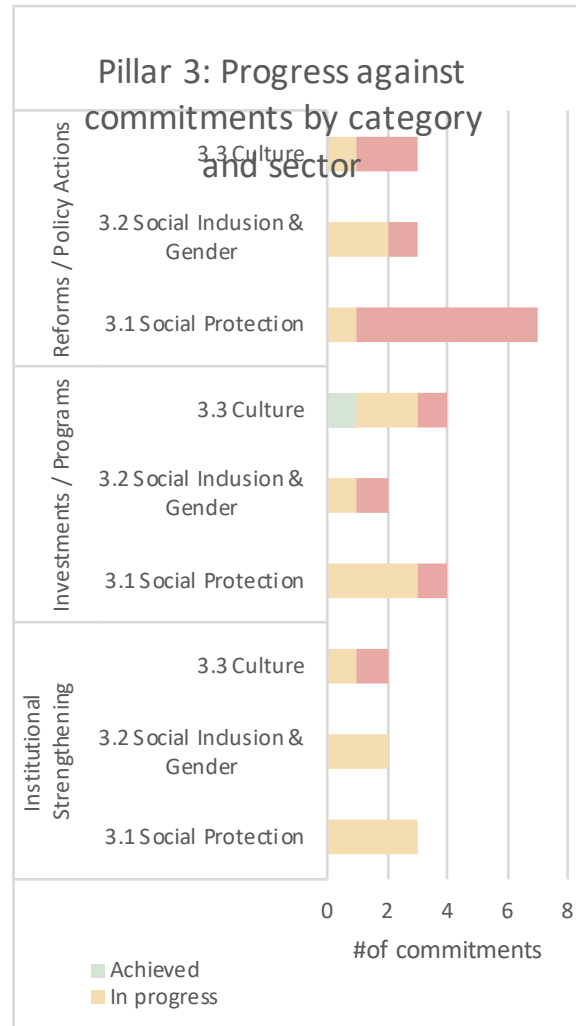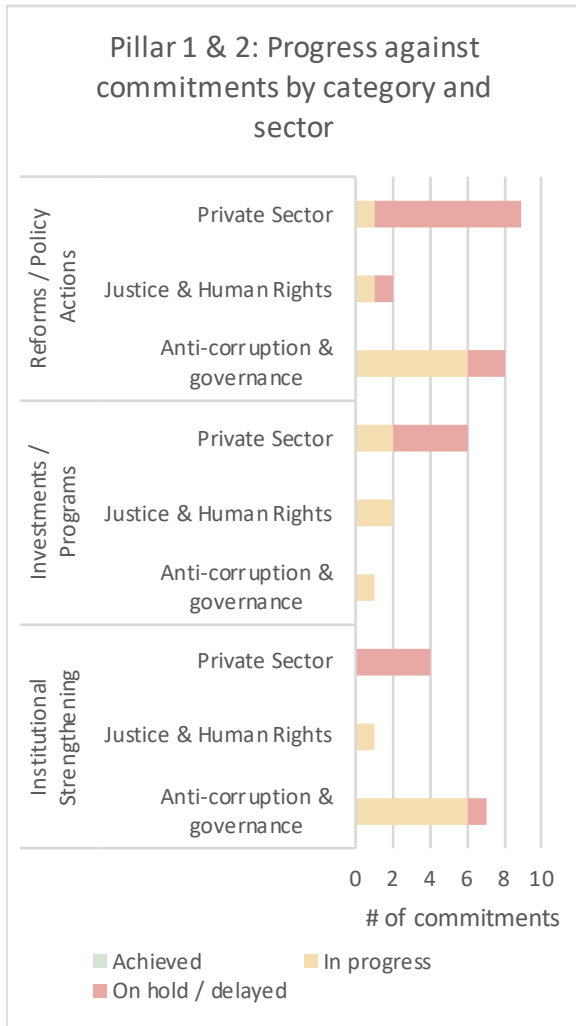

## DRAFT 3RF Sector Working Groups Monitoring Framework CG4

Working Group	Sector Lead	Sector Co-Lead
Pillar 1: Improving Governance		
Anti-Corruption Coordination Group (1.1 and 1.2)	World Bank	European Union
Justice & Human Rights (1.3)	UNDP	European Union
Pillar 2: Jobs and Growth		
Private Sector (2.1, 2.2. and 2.3.)	World Bank	UNDP
Pillar 3: Social Protection		
Social Protection (3.1)	European Union	World Bank, UNICEF & ILO (rotating)
Social Inclusion and Gender (3.2)	UN Women	European Union
Culture (3.3)	UNESCO	World Bank
Pillar 4: Improving Services		
Housing (4.1)	World Bank	UN-Habitat
Municipal services (4.3)	UN Habitat	World Bank
Port (4.2)	World Bank	ESCWA
Environment (4.3)	UNDP	World Bank
Electricity (4.3)	World Bank	ESCWA
Education (4.4)	Ministry of Education	UNICEF
Health (4.4)	European Union	WHO
Water (4.4)	European Union	World Bank

## DRAFT 3RF Sector Working Groups Monitoring Framework CG4

Members
<b>Governance and Accountability</b>
OMSAR, MoJ, BeyGov, MoFA, MoF, MoIM; UNDP, OHCHR, IOM, Democracy Reporting International, Gherbal, ALDIC
MoJ, MoL, MoIM; OHCHR, UNESCO, Legal Agenda, Legal Action Worldwide, USJ, Human Rights Watch, Justicia,
<b>Economic Opportunities</b>
MoET, MoI, MoFA, MoF; IOM, UNICEF, UNIDO, IDLO, EU, CSOs TBC
<b>Education, Inclusion and Culture</b>
MoSA, MoJ, MoL; UNHCR, UNRWA, IOM, WFP, LHIF, Oxfam, Save the Children, NRC, LUPD, ShareQ
MoSA, MoJ; UNDP, UNHCR, UNICEF, IOM, WFP, KAFA, LLWB
MoC, MoFA; UN-Habitat, BHI, BUL
<b>Services and Infrastructure</b>
BeyGov, BeyMay, Municipality; UNESCO, UNHCR, Beirut Heritage Institute, Beirut Urban Lab, Live Love, Beit el-Baraka
BeyGov, MoIM; UNICEF, UNOPS, CSOs
BeyGov, MoPW; CSOs, European Union
MoE UNOPS, UN-Habitat, Green Mind, IFI
MoF, MoPW; EDL, UNOPS, Lebanese Foundation for Renewable Energy, Issam Fares
MEHE UNOPS, UNESCO, European Union, LHIF, Qitabi
MoH; World Bank, UNOPS, IOM, UNICEF
MoE, MoPW, MoFA; UNOPS, UNICEF, UN-Habitat, LEWAP, Green Mind, Faraj el-Awar

**1.1 PFM and Public Procurement**  
Track 1 Commitments

Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.1.1	<b>In progress</b> Put in place enhanced fiduciary arrangements and oversight mechanisms for assistance funds to improve the transparency and accountability of the immediate recovery program. Ensure the inclusion of civil society and NGOs in the consultation and monitoring process.				The LFF oversight mechanisms are almost complete. Citizen engagement mechanisms are being developed. In addition, within each project's financing, additional accountability measures are designed to meet specific sectoral risks.	
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.1.2	<b>In progress</b> Publish a procurement plan, procurement notices, and future contract awards through an existing portal or new platform to improve transparency.				Central Tender Board portal is publishing notices of the activities that are under its mandate, as well as complying the procurement plans.	
Target date(s)						
Responsibility						
Track 2 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.1.3	<b>In progress</b> <u>Adopt the new Public Procurement Law</u> based on an inclusive revision process. In a second step, implement regulations and secondary legislation, including the mandatory use of revised Standard Bidding Documents; help ensure that these are ratified quickly.	<b>Achieved</b>  Public Procurement Law approved by Parliament				
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.1.4	<b>In progress</b> Formalize the Public Investment Management legal and regulatory framework, including guidelines and methodology, to improve efficiency in the use of reform and reconstruction funding.				The PIM work has been endorsed by the LFF partnership council as part of the governance pillar. The activities planned will be kicked off once the Request for Grant funding (GRF) within the World Bank is approve and funding is released.	
Target date(s)						
Responsibility						

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.1.5	In progress				Cabinet of Ministers is on a caretaker status, and Parliament is seldom convening. Thus, ratification of laws is delayed. Nevertheless, CoA is ready and has mobilized its team to start on building its capacity for forensic audits; awaiting LFF funding to kick off activities. Technical assistance for the Central Inspection is also included in the World Bank's LFF-funded governance activities. Focus of TA will be on strengthening CI's capacity in financial investigation.	
	Ratify the revised draft Court of Accounts Law to strengthen Lebanon's existing oversight function and develop standards and manuals for performance and forensic audits.					
Target date(s)						
Responsibility						
Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.1.6	In progress				The draft PPL stipulates the creation of the Procurement Policy Authority and the Procurement Review Board. In alignment with the draft PPL, TOR for both units are drafted as well as corresponding decrees under ongoing World Bank-funded activities.	
	Establish and operationalize a procurement regulatory body and a complaint handling unit to implement the new Procurement Law.					
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.1.7	In progress				The Public Procurement Strategy is developed and under final revision. Consultations will follow. In parallel, professionalization and e-procurement strategies are under development. All activities are under ongoing World Bank projects.	
	Undertake an inclusive process to develop and adopt a national public procurement strategy, including through professionalization of the workforce and advances in e-procurement.					
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.1.8	On hold / delayed				PFM reforms necessitate a strong commitment from Governmental stakeholders. Unfortunately, within a care-taker status, very limited engagement is observed by counterparts on the reforms front.	
	Establish a PFM Steering Committee that includes the Ministry of Finance, BDL, line ministries, and key oversight entities to improve transparency, accountability, and civil society participation in the public finance consultation process.					
Target date(s)						
Responsibility						

**1.2 Anti-corruption, Integrity & Transparency**

Track 1 Commitments

Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.2.1	In progress	Achieved				The LFF oversight mechanisms are almost completed. Citizen engagement mechanisms are being developed. In addition, within each project's financing, additional accountability measures are designed to meet specific sectoral risks. *Public awareness campaign on the access to information law designed and currently being executed by the ministry of information; Development of national guide for the implementation of the access to information law completed and deployment initiated. (UN)*
	Fully implement the Access to Information Law and related Action Plan as part of the effective and coordinated implementation of the National Anti-Corruption Strategy.	Adoption of the National Action Plan for implementation				
	Target date(s)					
Responsibility		UNDP + OMSAR				

Investments / Programs

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.2.2	In progress				UNDP Corruption Risk Management tool being applied in the Ministry of Social Affairs. UNDP and World Bank are exploring how to integrate risk management into the rehabilitation of the Beirut Port.	
	Design, integrate, and begin implementing corruption risk management programs that include an identification and assessment of key corruption risks, along with proposed risk management actions that will help prevent corruption during project implementation.					
	Target date(s)					
Responsibility		UNDP, Min of Social Affairs				

Institutional Strengthening

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.2.3	In progress	Achieved				*First progress report on the implementation of the National Anti-Corruption Strategy (2020-2025) developed, published, and discussed with civil society (UN)*
	Guarantee an effective enabling environment for independent nongovernmental organizations by facilitating civil society's access to information, officials, and Parliament; identify legal and regulatory obstacles that hinder civil society activities. Civil society should be empowered and invited to collaborate on monitoring and auditing of recovery and reconstruction activities.	EU and German funding programs designed to build capacity of civil society organizations for implementing and monitoring 3RF activities are underway.				
	Target date(s)					
Responsibility		EU, GIZ, CSOs				

Track 2 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.2.4	<b>On hold / delayed</b>					
	Facilitate an inclusive process for comprehensive electoral reform to enhance women's representation and participation.					
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.2.5	<b>On hold / delayed</b>					
	Increase transparency and efficiency, including through creation of an independent electoral management body.					
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.2.6	<b>In progress</b>	<b>In progress</b>	<b>In progress</b>		Judiciary has elected 2 judges as its nominees for commissioners on June 9, 2021. Cabinet of Ministers must select 4 additional Commissioners from Lawyers Association, Auditors, Bank Oversight and OMSAR nominees. World Bank, UNDP and others are prepared to provide technical assistance and capacity building to Agency as soon as it is created.	*Members of the National Anti-Corruption Institution appointed by the Council of Ministers and the first version of its internal and financial regulations are drafted in the framework (UN)*
	Select National Anti-Corruption Institution's commissioners and staff; develop their capacities and fully fund the Institution to accelerate implementation of the National Anti-Corruption Strategy.	Judges select 2 nominees. Cabinet of Ministers Secretariat prepares for selection of 4 additional nominees for Commissioner	Adoption of operating and financial regulations, appointment of Secretary General and provide budget			
Target date(s)						
Responsibility		Cabinet of Ministers	UNDP, WB, EU, CoM			
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.2.7	<b>In progress</b>	<b>In progress</b>				*Standard Operating Procedures for the whistleblower reception office (hosted by the ministry of justice) completed and adopted by the attorney general (UN)*
	Implement the Whistleblower Protection Law through adoption of decrees and standard operating procedures; conduct public awareness campaigns.	Deliver training guide and conduct first training for government officials				
Target date(s)						
Responsibility		UNDP, UNODC, MoJ				
Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
1.2.8	<b>In progress</b>	<b>In progress</b>	Not yet started	Not yet started	Legislative reforms to strengthen the Central Inspection and Court of Accounts remain stalled in the Parliament. The LFF Partnership Council has approved limited initial funding for World Bank technical assistance to help strengthen the capacity of the CoA (forensic audit) and the CI (financial inspections). Activities have been discussed and agreed with the CoA and CI. LFF funding made available in early November.	
	<b>Strengthen the independence and capacity of the Central Inspection and Court of Accounts by reviewing their legislative authorities and fully staffing these accountability institutions.</b>	<b>CoA:</b> Develop guides/manuals for forensic audit; <b>CIB:</b> Provide training on financial investigations	<b>CoA:</b> Conduct forensic audit training; <b>CIB:</b> Develop roadmap for systemic administration reforms	<b>CoA:</b> Conduct pilot forensic audit		
Target date(s)						
Responsibility		WB, CoA, CIB, Expertise France	WB, CoA, CIB, Expertise France			



1.3 Justice & Human Rights

Track 1 Commitments

Investments / Programs

Investments / Programs					
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status
1.3.1	In progress	Achieved	In progress	On hold / delayed	Milestone 1: With support of UNDP/OHCHR, the National Human Rights Commission (NHRC) has been monitoring the human rights situation post-blast and the commission published a report with its findings in July 2021. UNDP is supporting the set-up of NHRC's website, where the report will be uploaded. The EU, UNDP and OHCHR have initiated additional support to NHRC to increase capacity for both promotion and protection of Human Rights outside the scope of post-blast monitoring. Milestone 2: The budget has been prepared by NHRC and is included in the draft 2022 budgetary law. Until it is voted, NHRC has no funds. In addition to the vote of the budget, NHRC needs its internal regulations and financial regulations (by-laws) to be ratified by the Council of Ministers. Without such ratification, it will be incapable of accessing resources in the budget even if voted. Additional needs and opportunities for capacity building are currently being identified, considering the current operational and financial constraints. In this regard, a coordination structure has been established (UNDP, OHCHR, EU) and meets regularly. Milestone 3: More generally, the NHRC is still lacking a budget, an office and dedicated staff. Despite several attempts by NHRC leadership,
	<p><u>Support the National Human Rights Commission with adequate resources</u> to carry out its mandate to independently monitor the post-blast interventions of stakeholders, safeguard the rights of blast survivors, and identify systemic or widespread issues leading to human rights violations.</p>	Post-blast monitoring: NHRC's first report 'Monitoring Human Rights Violations in the Response to the Beirut Port Explosion' is published (in Arabic)	Resource allocation: A budget is prepared by NHRC, included in the draft 2022 budgetary law and voted on.	Premises: The NHRC is provided with adequate premises.	
Target date(s)	Q3 2022	Q3 2021 (July)	Q2 2022	Q3 2022	
Responsibility	NHRC, UNDP, OHCHR	NHRC, UNDP, OHCHR	NHRC, UNDP, EU, OHCHR, MoJ, MoF	PMO / MoJ	
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status
1.3.2	In progress	Achieved	Achieved	In progress	Milestone 1 & 2 : Programs/Activities supported by UNDP/BBA/USJ, EU, UNHCR, UNWomen, IOM, and UNESCO/UNODC/UNFPA have allowed for over 9000 individuals to be provided with free and comprehensive legal aid services. Milestone 3: With the needs shifting from immediate response to the blast to institutionalization of legal aid in Lebanon, larger focus will be put on the efforts spearheaded under the Access to Justice Working Group, led by the Ministry of Justice, and including both Bar Associations, UNDP and UNHCR. The Access to Justice WG, under the leadership of the MoJ, & including both Bar Associations, UNDP & UNHCR is developing and piloting a national strategy for legal aid. 3 Helpdesks have been established for the moment, with an expansion in the works
	Establish a program to provide comprehensive legal aid services to vulnerable individuals and groups, including women and children, in reconstruction areas. Assistance should include legal awareness and information sessions, legal advice and representation, as well as alternative dispute resolution services	Programmes to provide legal aid are established.	9,000 victims affected by the Beirut Port Explosion, have been supported through comprehensive legal aid services	A National Strategy for Legal Aid is developed & piloted, supported by the establishment of related Helpdesks	
Target date(s)	Q2 2022	Q4 2021	Q4 2021	Q4 2022	
Responsibility	UNDP, BBA, EU, OHCHR	UNDP/BBA/USJ, EU, UNWomen, IOM, UNHCR, UNESCO/UNODC/UNFPA	UNDP, BBA, EU, UNWomen, IOM, UNHCR, UNESCO/UNODC/UNFPA	MoJ, Bar Associations, UNDP, UNHCR	

Track 2 Commitments					
Reforms / Policy Actions					
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status
1.3.3	In progress	Achieved	On hold / delayed	On hold / delayed	Milestone 2: UNDP, EU, OHCHR are advocating with stakeholders to create a space for an inclusive and participatory discussion around the draft legislation (still not achieved). While stakeholders have been provided with opportunity to provide comments on a previous version of the draft law (judiciary independence), the opacity of the process remains cause for concern, and the draft continues to be questioned. Similar efforts will need to be put forth in order to secure the development and adoption of draft legislation on the Administrative and Financial independence. In February 2022 Parliamentary session, Draft law was to be put to a vote without stakeholders having the chance to review it. A one month delay was granted to allow for comments. MoJ formally sent the text (judiciary independence) to the Venice Commission in March 2022.
	Adopt the draft legislation that would strengthen the judiciary's independence, through a transparent process inclusive of civil society.	Draft law prepared: Draft Law on Judiciary independence has been finalized by parliamentary sub-Committee & transferred to Parliament plenary & circulated to stakeholders. Draft law on administrative independence has been transferred to Parliament Justice & Administration Committee for examination	Inclusive revision process in place: relevant stakeholders are provided with the opportunity to provide their comments on both draft laws in comprehensive and transparent manner	Adoption of Law: Both text draft laws are reviewed through an inclusive & comprehensive process, taking into account international standards, & adopted by Parliament	
Target date(s)	Q3 2022	Q4 2021	Q2 2022	Q3/Q4 2022	
Responsibility	MoJ, Parliament Administration & Justice Commission, UNDP	UNDP, EU, OHCHR, CSO Coalition	MoJ, Parliament, UNDP, EU, OHCHR, CSO Coalition, Venice Commission	MoJ, Parliament	
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status
1.3.4	On hold / delayed				Clarity on the content of the draft legislation mentioned above (Commitment 1.3.3) to inform the extent of necessary amendments.
	Amend relevant provisions of the Penal Code, the Code of Criminal Procedure, and the Law on Judicial Organization to empower the judiciary to carry out its mission and shield it from political interference and undue influence				
Target date(s)					
Responsibility					
Institutional Strengthening					
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description
1.3.5	In progress	In progress	On hold / delayed	On hold / delayed	Milestone 1: UNDP is supporting the High Judicial Council on the development of a transparent and efficient evaluation procedure for judges. A first draft has been completed by the dedicated working Group and is to be presented to the HJC leadership. UNDP is also supporting the development of a management database tool for the HJC. Milestone 2: With regards to the inspection authority, UNDP has initiated preliminary work on revising the inspection methodology. This process is delayed by the lack of availability of the Inspection Authority leadership. Milestone 3: WB has produced a series of Issue Notes to generate debate and discussions on improving access, efficiency and quality of Lebanon's justice system. EU has a forthcoming program on justice sector support aiming to respond to 3RF priorities. UNDP is expanding its support to the sector
	Strengthen bodies overseeing the justice system through objective and merit-based processes for selecting and evaluating judges, as well as enhanced management and oversight tools; provide them with sufficient resources to implement their mandate to safeguard the independence and effectiveness of the judiciary.	An evaluation process for judges is developed/A management database is developed to support the High Judicial Council (HJC)	The inspection methodology of the Inspection Authority is revised	New Programmes to support the sector are developed and implemented	
Target date(s)	Q4 2022	Q3 2022	Q4 2022	Q3, Q4 2022	
Responsibility	UNDP, EU, WB, High Judicial Council Inspection Authority	UNDP	UNDP	EU, WB, UNDP	



Additional notes / comments

Empty text area for additional notes or comments.

Additional notes / comments

Empty text area for additional notes or comments.

Additional notes / comments

Additional notes / comments

Additional notes / comments

2.1 Business Recovery & Jobs

Track 1 Commitments

Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.1.1	On hold / delayed				UN Results Report 2021 3RF: •83 shops rehabilitated and equipped in Karantina. 102 short-term jobs generated through the rehabilitation of the shops. 231 beneficiaries, of which 16 percent women, reached through the interventions in Karantina (16% women) •64 businesses received cash assistance support (through Al Majmoua) •Generated to date 7684 work-days benefitting 287 Lebanese and Syrian Workers on rehabilitation of a Police Station in Karantina	
	Launch short-term employment programs for provision of (i) cash support through cash-for-work, to support labor-intensive reconstruction activities, and (ii) intensive and quick trainings, to develop skills in relevant areas and professions. Special attention should be given to vulnerable groups, including women, youth, migrant workers, who have been hit hard during the crisis and are the most likely to face unemployment.					
	Target date(s) Responsibility					
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.1.2	In progress				B5 supports recovery of MSMEs and sustain the operations of eligible MFIs through the provision of grant support. The fund activities are also expected to preserve private sector jobs. The target size of the B5 Fund is US\$70 million, with the objective of supporting around 8500 damaged MSMEs. As a first phase, the B5 Fund will prioritize support to micro- and small firms (around 4000 MSE) and MFIs. Based on available funds at LFF, the fund will expand. The B5 will be financed through the LFF MDTF. The 3RF estimated the needs for MSMEs grants and TA at \$59,000. UNIDO project under preparation to provide support for SMEs and start-ups mainly in the agro-food business, through technology improvement, innovation, technical skills and adoption of circular economy principles within the framework of 3RF (in progress). One SME in the construction value	*Technology transfer and capacity building development. Support aims at sustaining productive jobs and improving the manufacturing capacity of small industries affected by Beirut blast. Berytech was contracted to implement an initiative that will help MSMEs affected by the Beirut explosion in the hospitality, design and crafts, food production and retail sectors. The project targets 40/50 SMEs in Karantina, Rmeil, Medawar and Geitawi (UN)*
	Provide businesses affected by the explosion with (a) grants to cover immediate reconstruction needs and (b) technical assistance to help them build back better, through the integration of environmental sustainability and technology transfer, the promotion of a better working environment, intangible needs including legal aid, and business development support services.					
	Target date(s) Responsibility					
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.1.3	In progress				The B5 will provide self-sustainability grants to MFIs to help them sustain their activities by covering part of their operational expenses over 6 to 12 months. The B5 has allocated \$7.5 M to support MFIs. The estimated needs in 3RF for the MFIs amount to \$20M, however these also include liquidity to MFIs to refinance portfolio of loans and extend new loans.	
	Provide liquidity to microfinance institutions to (i) channel funds to affected microenterprises; (ii) provide liquidity to MFIs (Micro-Finance Institutions) to disburse new loans to existing or new clients, and to reschedule the existing					
	Target date(s) Responsibility					

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.1.4	<b>On hold / delayed</b>					
	Support key value chains at firm and industry levels. This will include undertaking value chain assessments, which will identify the technical interventions required to strengthen affected sectors (e.g., construction value chains to meet reconstruction needs, cultural and tourism value chains to reposition the area as an attractive destination for visitors and tourists).					
Target date(s)						
Responsibility						

Track 2 Commitments

Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.1.5	<b>In progress</b>	<b>In progress</b>			An employment diagnostic analysis study is being implemented. However, the actual policy development and adoption is likely to be delayed in the absence of a properly functioning government. As soon as the diagnostic draft is ready (expected next month), related capacity building activities will be initiated and consultations with the social partners will be launched once circumstances become enabling to implement these activities. Also, the World Bank is developing a comprehensive analysis on the macro, supply (individual level) and demand (firm level) sides of jobs. The analytical report is expected to be finalized by December 2021. Based on this analysis, an evidence-based Jobs Strategy is planned to be developed. This proposed work will provide the Government of Lebanon with an analytical framework for identifying policies and	
	Develop a National Employment Policy for recovery to address employment and labor market challenges. It will include policy actions that address the repercussions of the multiple crises, in addition to addressing long-standing structural employment challenges.	Completed National Employment Diagnostic and launched national tripartite discussions around the results and capacity building for employer and worker organizations (UN)				
Target date(s)						
Responsibility						

Investments / Programs

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.1.6	<b>On hold / delayed</b>				IFC is in the process of setting up a financing facility that will provide blended concessional finance through various instruments including first loss risk sharing facilities and co-financing (debt or equity) instruments that support private sector investments.	
	Provide businesses affected by the explosion with concessional loans to support rehabilitation and restoring business activities. The financial support will cover both hard and soft costs (works, equipment, and working capital).					
Target date(s)						
Responsibility						

2.2 Financial Sector

Track 1 Commitments

Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.2.1	On hold / delayed	Not yet started				
	Strengthen the insurance sector through technical assistance in (i) claims settlement; (ii) solvency monitoring; and (iii) the development and financing of a potential "Advancing Policyholder Protection" scheme to provide direct assistance to policyholders in the event of a failed insurer, with the aim of protecting the most vulnerable retail clients.					
	Target date(s)					
Responsibility						

Track 2 Commitments

Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.2.2	On hold / delayed					
	Formulate an insurance development and restructuring strategy. This will include sector development with targeted solutions to protect MSMEs in the medium term. Work should commence immediately, with stakeholder engagement.					
	Target date(s)					
Responsibility						
2.2.3	On hold / delayed				IFC is in the process of setting up a financing facility that will provide blended concessional finance through various instruments including first loss risk sharing facilities and co-financing (debt or equity) instruments that support private sector investments.	
	Enact a new insurance law.					
	Target date(s)					
Responsibility						
2.2.4	On hold / delayed				The WB team provided regulatory guidance to Banque du Liban (BdL) on e-signature, based on which they'll conduct industry consultation and complete the drafting the regulations on electronic banking and financial services of Law 81. That said, DFS enablers and e-signature regulation are not developed and adopted.	
	Adopt basic regulatory enablers for DFS, including e-signature implementation					
	Target date(s)					
Responsibility						

**2.3 Business Enabling Environment**

**Track 1 Commitments**

Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.3.1	<b>On hold / delayed</b> Enact the long overdue insolvency and insolvency practitioners' law. Once it is approved, the government will need to draft and approve the executive regulations for both laws.					
Target date(s)						
Responsibility						

Investments / Programs

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.3.2	<b>On hold / delayed</b> Develop training curricula for insolvency practitioners and for judges, start building the capacity of judges on the new insolvency regime, and raise awareness with main stakeholders.					
Target date(s)						
Responsibility						

**Track 2 Commitments**

Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.3.3	<b>On hold / delayed</b> Develop and approve a comprehensive business environment action plan.					
Target date(s)						
Responsibility						
2.3.4	<b>On hold / delayed</b> Enact the draft competition law, including reforms to exclusive agencies; draft and approve executive regulations.	Not yet started				
Target date(s)						
Responsibility						
	<b>On hold / delayed</b>					



2.3.5	Approve a customs strategy as a first step to streamlining, automating, and reducing costs of trading across borders. The government will also need to inventory all administrative fee schedules, develop effective systems for risk management and post-clearance audits, and develop a national e-single window, to be implemented in the medium term.					
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.3.6	<b>On hold / delayed</b> Enact the long overdue secured transactions draft law. Once it is approved, the government will need to draft and approve its executive regulations.					
Target date(s)						
Responsibility						
<b>Institutional Strengthening</b>						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.3.7	<b>On hold / delayed</b> Establish and implement a solid governance/management structure for business environment reform. It should include an inter-ministerial reform committee headed by the Prime Minister, and corresponding technical working groups, with strong private sector participation.					
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.3.8	<b>On hold / delayed</b> Establish a well-functioning competition commission.					
Target date(s)						
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
2.3.9	<b>On hold / delayed</b> Following approval of the secured transactions law, establish and implement an effective electronic movable assets registry; begin raising awareness and developing the capacity of public and private stakeholders.					

3.1 Social Protection						
Track 1 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.1	On hold / delayed	In progress	In progress	In progress	<p><b>Milestone 1:</b> The 2022 draft Budget has been prepared and being discussed in Cabinet to then be presented to Parliament. From preliminary analysis, the budget does not contain needed reforms in social protection and inclusion. It includes a large program of cash transfers of one month base salary for 12 months to all public sector employees (civil, military, security personnel and retirees) - equivalent to 1% of GDP. The budget includes a small allocation for the NPTAs in previous years (social workers salary), and \$350 m for NSSF arrears. <b>Milestone 2:</b> Regarding unified registry, good progress has been made including commitment from GOL. A first time online Intake and Registration Platform (IRP) was developed and launched in December 2021 representing major step towards a unified social registry. The IRP is being used to identify potential beneficiaries for</p>	
	Prepare the 2021 budget and incorporate a strong program for social protection and inclusion; establish a unified registry of social assistance programs and put in place grievance redress, verification, and monitoring and evaluation systems.	Resources allocated by the government to poverty reduction programmes foreseen in 2022 Budget	Unified registry established	Grievance redress, verification and monitoring and evaluation in place for social assistance programmes.		
	Target date(s)	ASAP	ASAP	ASAP		
Responsibility		MOSA and PCM	MOSA and PCM	MOSA and PCM		
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.2	On hold / delayed	In progress	In progress		<p><b>Milestone 1:</b> 2022 budget was drafted by MoF and is currently discussed by the parliament. Expenditure review of social protection sector is completed by the UN (ILO and UNICEF) with Institut des Finances Basil Fuleihan. <b>Milestone 2:</b> The World Bank is finalizing the Public Finance Review exercise and results will be made public soon. It provides concrete short, medium, and long term recommendations for social protection programs.</p>	
	Identify fiscal space in the annual budgets for social protection, particularly for increasing expenditure allocations for social assistance programs; and plan to ensure the short-term financial viability of existing social security institutions.	Social protection resources foreseen in 2022 Budget	Social protection financing strategy in place			
	Target date(s)	ASAP	ASAP			
Responsibility		MOSA and PCM	MOSA and PCM			
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.3	Achieved	Achieved			<p>Subsidies were largely removed by Q3 2021. A reform plan was prepared by Diab government and Parliament passed the Ration Card Law 230 in July 2021. However, the removal of FX subsidies was disorderly and chaotic and did not align with implementation of a large-scale safety net program. Some analysis on impacts was completed (lack of micro data however hampers solid impact analysis). Registration for the Ration Card (BCCT) started in December 2021, and closed on 31 January 2022 with more than 580,000 households registered (for both ESSN and BCCT). GOL has officially requested financing from the WB for the ration card.</p>	
	Provide a new strategic direction for the reform of price subsidies (including electricity, fuel, pharmaceutical products, and subsidized housing loans); analyze the impact of removing subsidies on prices and well-being; design an effective transition for reform that promotes progressive fiscal resource use while implementing mitigation measures to protect the poor, the vulnerable, and the middle class.	A strategic direction for reform of price subsidies is approved and implemented.				
	Target date(s)	Done				
Responsibility		Done				
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.4	In progress	Achieved	In progress	In progress	<p><b>Milestone 1:</b> Blast Emergency Cash Transfer is complete, and reached its target of 80,000 individuals in vulnerable groups. The design of the Social Grants programme is underway, with the Disability Allowance due for launch early 2022. UNICEF's child grant known as Haddi also began registration in May and was launched in June 2021. The programme is now reaching 115,000 vulnerable individuals with monthly cash transfer in US\$. <b>Milestone 2:</b> Expansion of NPTP with funding from EU, Germany, Canada, France, Ireland, Italy, and Norway, and via WFP implementation, is continuing and has so far reached 36 000 families. Ration cards program launched its registration in Dec 2021. <b>Milestone 3:</b> Consultations on design of national Social Pension scheme underway.</p>	
	Scale up social assistance interventions and their systems to alleviate the impact of the explosion in affected areas through cash transfer programs, with a focus on economically vulnerable individuals (particularly older persons, persons with disabilities, women, and children); accelerate the expansion of the National Poverty Targeting Program (NPTP).	Blast cash response completed by Q1 2021.	NPTP scale up to 75,000 families (now 36 000)	Social grants based on lifecycle vulnerabilities are designed.		
	Target date(s)	Done	Q2	Q2		
Responsibility		Done	EU and WFP	ILO		

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.5	<b>On hold / delayed</b>	<b>On hold / delayed</b>			On hold due to no resource allocated for technical assistance in this area	
	Extend an injury/death compensation scheme for those affected by the blast and not covered by insurance.	Compensation scheme in place				
	Target date(s)	Not clear				
Responsibility		Not clear				
<b>Institutional Strengthening</b>						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.6	<b>Achieved</b>	<b>Achieved</b>			The SSN Partners Forum has been expanded to cover the entire sector of Social Protection, in line with the 3RF Pillar III. The Forum will meet regularly to ensure coordination among donors, UN, WB, and NGO actors. The 3RF technical team is leading on the multi-stakeholder platform for 3RF as a whole. For social protection, two existing platforms for civil society have finalised position papers.	
	Establish a multi-stakeholder platform to promote coordination, cohesion, and collaboration across various actors in the social protection sector.	The Social Protection Forum is established				
	Target date(s)	Done				
Responsibility		EU				
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.7	<b>In progress</b>	<b>In progress</b>			Under the ESSN, the development of robust social assistance systems are supported and under implementation. Achieving these commitments is also the objective of the EU's support to the NPTP and the roll out of the social grants programme. The DAEM Intake and Registration Platform - on the IMPACT Platform - under the supervision of the Central Inspection - was developed with technical assistance from the World Bank as a unified entry point for citizens for social assistance. Development was financed from the ESSN as building this system represent an entry point towards building the unified social registry. However a unified registry is needed ultimately overall for linking all programmes, not only for the anti-poverty programmes	
	Support government to prioritize investments to develop social assistance systems, including grievance and redress systems, and verification; put in place anti-corruption measures to ensure that the governance of any social protection program is transparent, participatory, evidence-based, and sustainable; invest in data systems, registries, and development of a unified registry for all social protection programs.	NPTP: developing an MIS, institutionalising the GRM, and the monitoring and evaluation tools.				
	Target date(s)	Q2				
Responsibility		World Bank (ESSN) and EU (NPTP)				
<b>Track 2 Commitments</b>						
<b>Reforms / Policy Actions</b>						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.8	<b>In progress</b>	<b>Achieved</b>	<b>In progress</b>	<b>In progress</b>	<b>Milestone 1:</b> The National Social Protection Strategy is drafted and submitted to Prime Minister upon which a technical committee involving key line ministries was formed to discuss and approve the Strategy Document. <b>Milestone 2:</b> The first meeting has not been convened yet. <b>Milestone 3:</b> Work to support implementation of the SP Strategy (once finalized and adopted) is being putting in place.	
	Finalize and approve the National Social Protection Strategy, adopting a rights-based, comprehensive, and inclusive approach – including linkages to the social assistance system that is in place for refugees; address the need for universal access through a combination of contributory and non-contributory mechanisms, encompassing the five social protection components listed above.	The National Social Protection Strategy drafting is completed	The National Social Protection Strategy is approved by the Inter-Ministerial Committee on Social Policy	The National Social Protection Strategy's implementation plan is drafted		
	Target date(s)	Done	ASAP	ASAP		
Responsibility		Done	MOSA and PCM	MOSA and PCM		
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.9	<b>In progress</b>	<b>In progress</b>			A reform plan was developed a year ago by WB and MoF. It is currently being updated with new data and macro indicators.	
	Finalize reforms of public sector pensions to reduce inequities across social insurance schemes and enhance long-term sustainability.					
	Target date(s)	Q2				
Responsibility		World bank and MoF				

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.10	On hold / delayed	In progress	In progress	In progress	A draft law for unemployment insurance has been produced by MoL and NSSF and debate in the relevant parliamentary committee has started in Jan 2022. The draft law for EOSI is now complete (pending institutional chapter, which is now being considered by the parliamentary committee). Mechanism for transitional arrangements for short-term fixes to EOSI scheme under discussion.	
	Expand the adequacy and comprehensiveness of social insurance benefits of the <b>National Social Security Fund</b> (end-of-service reform and introduction of unemployment insurance);	Draft legislation for EOSI reform and unemployment insurance completed	Legislation for EOSI reform and unemployment insurance approved	Implementation of new pension system and unemployment insurance started		
	Target date(s)	Q2	Q2	Q2		
Responsibility		ILO	ILO	ILO		
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.11	In progress	Achieved	In progress		A financial assessment of the NSSF is underway and will produce an analysis of asset-liability match and financial outlook for the next 5 years. Analysis expected to be completed by the end of Q1 (2022)	
	Develop a plan to ensure financial sustainability of the <b>National Social Security Fund (NSSF)</b> and extend contributory benefits, following an external audit; reform NSSF governance.	Financial assessment of the NSSF completed	Recommendations of the financial assessment discussed and adopted			
	Target date(s)	Done	Q1			
Responsibility		Done	MOSA and PCM			
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.12	In progress	In progress	In progress		<p><b>Milestone 1:</b> NPTP is being scaled up from the current 36 000 households to an expected 75 000 households by the beginning of 2022. ESSN has been approved by Parliament and registration took place between December 1 2021 and January 31, 2022. Payments for first batch of ESSN beneficiaries expected to start early March and to reach all 150,000 extreme poor households by June 2022.</p> <p>(ii) The Social Grants programme is about to start with the Disability Allowance due for launch early 2022 as design work is being finalized. The programme integrates a component of linkages to other complementary services. (iii) the Haddi child grant was launched in June 2021 and now reaches over 115,000 vulnerable individuals. Provision of protection services by UNHCR in the affected blast area through regular partners, regardless of whether the beneficiaries have been personally affected by the blast. (iv) Consultations on design of national Social Pension scheme underway.</p> <p>(v) Financial access to health and education is still limited</p>	
	Establish the foundations of a social assistance system by (i) providing cash transfers at scale to extremely poor households through the ongoing scale-up of the National Poverty Targeting Program and forthcoming Emergency Social Safety Net; (ii) introducing social grants to address life-cycle vulnerabilities (old age, disability, and child-related vulnerability, with progressive implementation); (iii) linking social assistance to other services, as well as to social assistance for refugees, which needs to be expanded to meet increased needs; and (iv) expanding financial access to health and education.	NPTP provides cash transfers for 75 000 families. Child grant launched under Haddi. National Disability Allowance designed.	ESSN provides cash transfers to 147,000 extreme poor households and education top ups to 87,000 (13-18) children enrolled in public schools.			
	Target date(s)	Q2	Q2			
Responsibility		MOSA and PCM	MOSA and PCM			
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.13	In progress	Achieved	In progress		Expenditure review of social protection sector is completed by the UN (ILO and UNICEF) with Institut des Finances Basil Fuleihan.	
	Review and expand spending on social welfare services; rationalize and reallocate in line with the assessed, unmet needs of individuals and households for preventive and specialized care as well as case management.	Expenditure review of social protection sector is completed by the UN (ILO and UNICEF) with Institut des Finances Basil Fuleihan.	As part of Social Protection Strategy			
	Target date(s)	Done	Q2			
Responsibility		ILO and UNICEF with Institut des Finances Basil Fuleihan.				
Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.1.14	In progress	In progress			The next Inter-ministerial Committee on Social Policy meeting / Technical Committee formed by the PM is scheduled for beginning February 2022 to review the National SP Strategy.	
	Recommence institutional coordination at the policy level; within the purview of the Government Inter-ministerial Committee on Social Policy, oversee completion and implementation of the national social protection strategy and financing plan, as well as policy and program monitoring.	Inter-ministerial Committee meetings are held regularly.				
	Target date(s)	Q1				

3.2 Social Cohesion, Inclusion & Gender

Track 1 Commitments

Investments / Programs

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.2.1	<b>In progress</b> Support the immediate provision of, and access to, protection and social welfare services for vulnerable groups affected by the blast. This includes case management, protection, prevention, response, and psychosocial support; sexual and gender-based violence prevention and response services; child and older person care services; and access to safe spaces. Interventions will address barriers that affect marginalized groups' equal access to assistance, such as strengthening outreach.	<b>Achieved</b> 40 creative expression activities with 773 participants, especially children and youth, to support psycho-social recovery from the blast are implemented in Karantina	<b>Achieved</b> The LFF project "Support for Social Recovery Needs of Vulnerable Groups in Beirut" is signed to support survivors of SGBV, people suffering from deteriorated psycho-social wellbeing, persons with disabilities and older persons	<b>In progress</b> Emergency support incl. food, temporary cash assistance, household rehabilitation, legal aid, psycho-social support, & medication is provided to families and individuals in the blast affected areas	There are many CSOs providing services throughout the country which should be mapped and captured through the WG. There remains limited governmental/public support for these critical protection and social services, and these services continue to be the leading responsibilities of Lebanese and international organizations. Milestone 2: The LFF Social Recovery Services Project was signed off by the Prime Minister and the WB on 25.02.2022. Milestone 3: Emergency support services are being provided to families and individuals including women, girls, LGBTQIA+ community members, people with disabilities and migrant workers.	Milestone 1: Production of a book telling the stories of the people of Karantina "The Living of Al Karantina" and setting up of The Memory Box in Karantina <a href="http://bit.ly/Karantina2021">http://bit.ly/Karantina2021</a> ; Milestone 2: See details of the LFF project here: <a href="https://www.rescue.org/resource/supporting-beirut-immmediate-social-recovery-services-environmental-social-standards-all">https://www.rescue.org/resource/supporting-beirut-immmediate-social-recovery-services-environmental-social-standards-all</a> Milestone 3: See details of the project here: <a href="https://www.oxfam.org.uk/media/press-releases/queer-communities-at-huge-risk-in-lebanon-oxfam-warns/">https://www.oxfam.org.uk/media/press-releases/queer-communities-at-huge-risk-in-lebanon-oxfam-warns/</a>
Target date(s)	Q4 2022	Q4 2021	Q1 2022	Q2 2022		
Responsibility	UN Women, UNDP, CSOs	UNDP	IRC, NGOs, WB	Oxfam & 11 partners		

Institutional Strengthening

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.2.2	<b>Achieved</b> Establish a multi-stakeholder platform to promote coordination, cohesion, and collaboration across various actors in the social protection sector.	<b>Achieved</b> The 3RF Social Cohesion and Inclusion, and Gender Working Group is established as a multi-stakeholder coordination platform			The social, cohesion, inclusion and gender equality (SCIG) Working Group (WG) convened for the first time on 05.11.2021, and has since convened again on 20.01.2022. It continues to circulate information relevant to the 3RF priorities between the WG members, which includes UN Women, EU, KAFA, LLWB, OXFAM, UNFPA. Priority of the WG for 2022 is to coordinate with other relevant WGs, especially the 3RF Social Protection WG and other Gender WGs, and convene thematic WG meetings with additional invitees where relevant (e.g. from NCLW) dedicated to each commitment outlined here.	
Target date(s)	Q4 2021	Q4 2021				
Responsibility	UN Women	Co-leads: UN Women & EU				

Track 2 Commitments

Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.2.3	<b>In progress</b> Pass legislative and policy reforms to reduce the structural barriers that prevent marginalized groups from equally accessing services, assistance, and human rights. Pursue urgent reforms to enable a political and social environment that is socially inclusive, cohesive, and gender equitable, such as passage of the anti-sexual harassment law; repeal Article 534 of the penal code to tackle homophobic and gender-based discrimination; reform the Kafala system and implement the standard unified contract by the Ministry of Labor.	<b>Achieved</b> A charter of demands calling for a gendered blast response plan as well as a list of legislative and policy reforms for a fair and equitable space for women in public life are issued	<b>Achieved</b> A legal study that analyzes the jurisprudence under Law 293/2014 on domestic violence & of various Lebanese religious courts pertaining to family law matters with elements of domestic violence is conducted & published	<b>In progress</b> A GBV Task Force composed of attorneys willing to adequately represent survivors of GBV before competent authorities is created	The WG needs to agree which reform specified in this commitment it should focus on, and with what kind of milestone(s). Milestone 1: With the support of UN Women, the Feminist Civil Society Platform issued a Charter of Demands calling for a gendered response plan and also issued a list of legislative and policy reforms for a fair and equitable space for women in public life including gender quota - see: <a href="https://lebfemcsp.com/statement/">https://lebfemcsp.com/statement/</a> Milestone 2: The aim of this study was to identify legal gaps in the practices of judges and courts, in an effort to improve the outcome of cases for survivors of domestic violence in the fight against gender-based violence - see publication: Enhancing Access to Justice for Survivors of Domestic Violence Before Lebanese Courts.	
Target date(s)		Q4 2021	Q3 2021			
Responsibility		Feminist Civil Society Platform &	Expertise France, EU4WE			

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.2.4	<b>In progress</b> Adopt an inclusive fee waiver for obtaining and renewing temporary legal residency permits for refugees, to enable their access to services and civil documentation.	<b>In progress</b>	<b>On hold / delayed</b> All Syrians registered with UNHCR are allowed to obtain a free legal residency regardless if they previously renewed their residency based on sponsorship		Based on a government decision, GSO issued a circular stating that Syrians in Lebanon who are holders of a valid UNHCR certificate may be granted temporary residency, free of charge and renewable several times, and not subject to late fees, provided they meet certain conditions - i) UNHCR certificate prior to 1/1/2015 ii) have not previously obtained residency based on pledge of responsibility (work or personal) or through title deed or rental contract. Way forward, all Syrians registered with UNHCR should be allowed to obtain a free legal residency regardless if they previously renewed their residency based on sponsorship. However, during the reporting period progress has been stalled by increasing anti-refugee rhetoric by the government, specifically a newly proposed draft law that prevents refugees	
Target date(s)	Q4 2022?	?				
Responsibility	UNHCR, GoL	UNHCR	GSO			
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.2.5	<b>On hold / delayed</b> Develop reforms initiatives that institutionalize the right to know, right to justice, and right to reparations: these must be developed to help deal with consequences of the explosion.				Reforms still not adopted-Though the National Commission for Missing and Disappeared has been established to follow up on the implementation of Law 105. While this is for the missing during the Lebanese civil war and gives the right to know to victims' families, but it does prepare the ground for the spread of the culture of transitional justice in the country. The WG needs to agree on milestones linked to this commitment.	
Target date(s)						
Responsibility						
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.2.6	<b>In progress</b> Promote the sustainability of service provision by reinforcing the role of the Ministry of Social Affairs and its Social Development Centers (SDCs) in providing social welfare and protection services; invest in capacity- building for local government and civil society organizations and systematize linkages between SDCs and CSOs (Civil Society Organizations) for more efficient delivery of services.	<b>In progress</b>	<b>Not yet started</b> A mapping of CSOs' provision of protection and social welfare services for vulnerable groups affected by the blast provides visibility of achievements and a baseline for remaining needs to be addressed	<b>Not yet started</b> Priority actions that the SCIG WG can work on to further this commitment are identified through coordination with the 3RF Social Protection WG	Given the crisis for MOSA and SDC staff, large investment in service delivery strengthening for the SDCs is on-hold. The majority of social and protection services have been observed to be provided at CSOs premises. Thorough mapping and assessment is a need to understand the best way forward for this intervention. Projects and efforts are on-going. Multiple NGOs, INGOs and other international institutions are continuing to support MoSA to provide essential service delivery and build the capacities of public officials to respond to the crisis through staffing, capacity building, and equipment. Supporting service provision and capacity interventions through MOSA has been made nearly impossible with the wage reduction of public servants, closure of SDCs due to strikes and COVID measures. As a result it seems that more and more NGOs are providing services in their own centers, with less coordination with SDCs	
Target date(s)	Q4 2022	Q4 2022	Q3 2022?	Q2 2022		
Responsibility	EU, UN Women, CSOs	I/NGOs, Int. institutions	UN Women, EU, CSOs	EU, UN Women, CSOs		
Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.2.7	<b>In progress</b> Build the capacity of institutions and civil society to restore community-state relations, reduce community tensions, support victims' rights and reparations, and protect vulnerable groups; support existing dialogue platforms that work to foster social stability and cohesion at the national and local levels.	<b>Achieved</b> 1559 community members residing in blast-affected areas have been engaged through dialogue platforms & community groups that advocate for the protection & inclusion of vulnerable groups & resolve disputes	<b>In progress</b> Locally lead initiatives aimed at fostering social cohesion and stability, and preventing tensions are supported		Work on social cohesion continued both at local and national level through locally lead initiatives as well as through media and education- a Social Cohesion assessment was conducted to explore new areas of work in light of recent development in the country. Efforts are ongoing, whether between civil society actors through several dialogue platforms or between local actors and municipalities at local level working on mechanisms for social stability, aiming at preventing tensions but also on building trust by communities and local governments through frameworks for direct communication; participation in decision making and in addressing needs.	Milestone 1: In four communities, local women mediators have resolved disputes and diffused tensions related to the fuel crisis and other community issues in schools and between youth, in addition to spreading awareness on a culture of mediation to community leaders and members.
Target date(s)		Q4 2021	Q4 2022			
Responsibility		UN Women, 6 CSOs	UNDP, CSOs, municipalities			

### 3.3 Culture

#### Track 1 Commitments

##### Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.3.1	In progress	In progress	Achieved	In progress	<p>Milestone 1: A preliminary strategy on interventions of urgent protection and inventory for tangible cultural assets were completed with UNESCO, DGA, BBHR 2020 and BHI. Milestone 2: UNESCO-DGA 3D georeferenced urban and built heritage modelling was launched and is being fed with regular updates (the modelling includes technical surveys, including those conducted on specific buildings). Milestone 3: The LFF-financed Beirut Housing Rehabilitation and Culture and Creative Industries (CCI) Recovery Project was signed by WB and PM on 25.02.2022</p>	<p>See LFF Project details:  <a href="https://www.worldbank.org/en/news/press-release/2022/02/25/lebanon-financing-facility-supports-housing-reconstruction-cultural-and-creative-industries-and-social-recovery-needs">https://www.worldbank.org/en/news/press-release/2022/02/25/lebanon-financing-facility-supports-housing-reconstruction-cultural-and-creative-industries-and-social-recovery-needs</a></p>
	Develop a strategy and detailed assessment on urgent measures for conservation and rehabilitation of historic buildings and conservation guidelines.	A finalized strategy on interventions of urgent protection and inventory for tangible cultural assets is completed	UNESCO-DGA 3D georeferenced urban and built heritage modelling is launched.	The LFF 'Beirut Housing Rehabilitation and Culture and Creative Industries Recovery' project has provided an assessment of rehabilitation measures for prioritized historical housing for the most vulnerable people, located within 5km of the epicenter of the Beirut Port Explosion		
	Target date(s) Q4 2022	Q3 2022	Q4 2021 (Oct)	Q2 2022		
Responsibility	UNESCO, BBHR, BHI, DGA	UNESCO, BBHR 2020, BHI, DGA	UNESCO-DGA	UN Habitat		
<b>Investments / Programs</b>						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.3.2	In progress	Achieved	Achieved	In progress	<p>Stakeholders' mobilization, including pro-bono operating private sector, NGOs, and youth volunteering-led initiatives enabled to almost complete the emergency phase of urgent propping, sheltering and emergency consolidations of heritage buildings at risk of collapse (65 buildings), with several minor repair conducted at heritage buildings. In total, BHI completed 22 intervention on 18 buildings with the support of ALIPH, and with BBHR20 as the consultants. ALIPH sheltered 12 historical houses. These mainstreamed efforts of various operating partners on the ground have been conducted in coordination with the DGA and local authorities. UNESCO-DGA have dealt particularly with 13 heavily structurally affected buildings.</p>	<p>Milestone 1: See ALIPH's work: <a href="https://www.aliph-foundation.org/en/projects/urgent-stabilization-of-historical-houses-in-rmeil-and-medawar-quarters">https://www.aliph-foundation.org/en/projects/urgent-stabilization-of-historical-houses-in-rmeil-and-medawar-quarters</a>; See BHI's work: <a href="https://beirutheritageinitiative.com/our-projects/">https://beirutheritageinitiative.com/our-projects/</a>                      Milestone 2: See Live Love Beirut's annual report: <a href="https://livelove.org/report2021">https://livelove.org/report2021</a></p>
	Implement shoring up, sheltering and urgent protection measures to prevent collapse of heritage buildings, as well as immediate conservation and safeguarding to avoid loss of tangible and intangible assets; involve all stakeholders, including civil society organizations.	The emergency phase of urgent propping, sheltering and emergency consolidations of 65 heritage buildings at risk of collapse is completed in coordination with the Directorate General of Antiquities (DGA)	25 heritage buildings are renovated by different private initiatives and NGOs. 2,000 heritage housing units are renovated in coordination with DGA and local authorities in Medawar, Rmeil, and Achrafieh.	Remaining rehabilitation priorities are identified and addressed with the support of the LFF financed project in coordination with CSOs and DGA		
	Target date(s) Q4 2021	Q3 2021	Q4 2021	Q4 2022		
Responsibility	DGA, BHI, UNESCO, LLB, Beit el Baraka. ALIPH, IFPO	NGOs, pro-bono private sector,	BHI, Live Love Beirut, Beit el Baraka	UN Habitat, CSOs, WB		
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.3.3	In progress	Achieved	Achieved	On hold / delayed	<p>Milestone 2: The BHI manuals as well as the presentations are available online and for free at: <a href="http://beirutheritageinitiative.com/restoration-manual/">beirutheritageinitiative.com/restoration-manual/</a> Funded by Fondation de France. Milestone 3: Intangible Cultural Heritage (ICH) still requires a systematic assessment to inform/strengthen community-led mechanisms and initiatives. EU: implementing partner currently finalizing the assembling of the team to work on the project - will assemble at the end of February and begin the project in March 2022.</p>	
	Carry out emergency management measures, inventories of tangible and intangible heritage assets, and immediate conservation measures to avoid loss.	A quick damage assessment on intangible cultural heritage in the damaged areas has been conducted with urgent needs identified, and activities devised for their	Two manuals on restoration and conservation methods of traditional and modern heritage respectively are developed, published, and presented online with architects, restorers and engineers	A systematic assessment to inform/strengthen community-led mechanisms and initiatives to conserve ICH is conducted		
	Target date(s) Q4 2022	Nov/20	Q3 2021	Q4 2022?		
Responsibility	UNESCO, BHI, DGA	UNESCO	BHI			

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
3.3.4	In progress	Achieved	On hold / delayed	In progress	Milestone 2: Only little support has so far been possible to CCI (i.e. UNESCO, Goethe Institute, Prince Claus Foundation, Aliph) due to limited funding, compared to the needs identified to revitalize the sector. Milestone 3: WB has worked with UN-Habitat in conducting a preliminary survey of CCI practitioners and entities in the 5 km affected by the Port of Beirut explosion. The LFF project includes a dedicated component on emergency support for CCI recovery that will provide grants to eligible CCI practitioners and entities affected by the Port of Beirut August 4, 2020, explosion.	Milestone 1: TERDAD festival: UNESCO provided urgent financial assistance to 5 local cultural organizations involved in different sectors of Culture, who in their turn supported local artists & other organizations through a coproduction program. The festival included 16 artistic shows & 11 training workshops. Some activities continued after the festival, with six additional artistic performances & assistance to artists and students in artistic fields to produce their work.
	Assist artists, cultural producers, and community-led initiatives to restart cultural activities and production in public and cultural spaces that serve affected communities (through grants and priority rehabilitation and refurbishment of galleries, workshops, theaters, and other spaces); help cultural activities and CCI businesses resume operation, in temporary venues as needed, particularly to protect their high share of skilled youth employment.	The 3-day Terdad Festival of public cultural activities in Mar Mikhael, Gemmayze, Karantina, and Surssock has taken place supporting 15 cultural NGOs, 200 artists, technicians, & cultural agents and followed by 3,200+ participants	A mapping of the cultural and creative industries provides a basis for identifying priority support needs	Approx. 1,300 CCI actors affected by the Beirut Port Explosion are supported through the LFF Project with grants, outreach, and awareness raising		
	Target date(s)	Q3 2021 (Jul)		Q4 2024		
Responsibility		UNESCO, NGOs		UNESCO, WB		
<b>Institutional Strengthening</b>						
3.3.5	In progress	Achieved	In progress		The main focus is on the transitional law n.194 entrusting MoC/DGA to elaborate the protection and rehabilitation plan of the damaged area (Art.7). This commitment is closely linked with the establishment of the Planning and Coordination Unit (PCU) currently being worked on by the Housing and Municipal Services Working Groups, with input from Culture sector experts	
	Deliver capacity building and technical assistance to enforce adequate legal measures to prevent demolition and to enable municipal staff to inspect and enforce guidelines; establish a municipality One-Stop-Shop with sub-windows (e.g., building permits, incentives).	The urban heritage attributes of Beirut's damaged areas are identified in order to map all heritage assets in preparation for the action plan as per law 194 - article 7.	The Ministry of Culture and DGA is provided adequate technical assistance in order to devise the action plan as per law 194.			
	Target date(s)	Dec/21	End 2022			
Responsibility		UNESCO-DGA-AUB	UNESCO-DGA			
3.3.6	In progress	In progress	Achieved	In progress	Milestone 1: To date, BHI has collaborated with LLB and HOC for the Ghoniam Cluster, LLB for the renovation of one house in Mar Mikhael, and LLB + BeB for another building in Mar Mikhael. Milestone 2: The 3D georeferenced documentation on the damaged areas and the Mapping data produced by the AUB urban Lab were submitted by UNESCO to the DGA as the main beneficiary. These data are available upon request from DGA. Under the LFF project: an extensive outreach and communication campaign will be conducted to reach out to cultural entities and practitioners operating in Beirut and to raise awareness about the Beirut Housing and CCI Recovery Project. The campaign will be rolled out by a local organization for communications and awareness raising. Milestone 3: The website was launched in March 2022, it continues to be populated with data and its	Milestone 3: The BUO's website can be seen here: <a href="https://experience.arcgis.com/experience/e18c14bd7b864c36876fef4a0725cec5/page/Page-1/?views=Individual-NGOs">https://experience.arcgis.com/experience/e18c14bd7b864c36876fef4a0725cec5/page/Page-1/?views=Individual-NGOs</a>
	Put in place mechanisms and develop local initiatives to promote and support community engagement for coordination, advocacy, and communication.	A CSOs platform for coordination, sharing challenges/ideas, seeking support etc. is created	Data and maps produced by international organizations are accessible to all CSOs an open source (cf. UNESCO's mapping data).	A website that maps repairs carried out by various actors (I/NGOs, international orgs. etc) is developed, populated with data, and used to coordinate on remaining needs for (heritage) housing repairs		
	Target date(s)	Q2 2022	Q3 2021	Q2 2022		
Responsibility		UNESCO, CSOs, WB	UNESCO	Beirut Urban Observatory		
<b>Track 2 Commitments</b>						
<b>Reforms / Policy Actions</b>						
3.3.7	On hold / delayed	On hold / delayed			Milestone 1: Built Heritage Law (2016-2017) still pending approval. Negotiations for cultural enabling environment are ongoing. Commitment 3.3.5 feeds into this commitment 3.3.7 (focus on the implementation of the transitional law n.194.)	
	Approve the new heritage law, which remains pending approval – targeting building owners, tenants, and investors; strengthen the enabling environment to engage with the owners of heritage buildings; structure a regulatory framework that outlines adequate technical assistance; provide incentives and subsidies for rehabilitation. Ensure that the heritage law's measures are reflected in urban regulations and master plans.	Built Heritage law is adopted				
	Target date(s)					
Responsibility		Ministry of Culture				



	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
S.S.	In progress	In progress			Milestone 1: Negotiations with the Ministry of Culture regarding the ratification of the Convention are underway	
	Carry out a baseline study on the parameters of the creative economy and its legal and regulatory framework to support broad reform that recognizes CCI as an emerging sector, eases regulatory burdens, promotes competition, and supports public and private sector investment. Ensure adequate institutional set-up to promote implementation of decisions and laws.	Lebanon ratifies The Convention on the Protection and Promotion of the Diversity of Cultural Expressions (2005)				
	Target date(s)					
Responsibility		UNESCO-Ministry of Culture				
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
S.S.	In progress	In progress			Volunteering works and substantial private sector contribution have been provided for emergency interventions.	
	Rehabilitate and repair assets to restore functions as soon as possible, ensuring provision of a minimum wage to cultural creators and technicians, who are often freelancers without any formal job status.	The Sursock museum is rehabilitated and able to function again				
	Target date(s)	Sep/22				
Responsibility		UNESCO				

4.1 Housing

Track 1 Commitments

Reforms / Policy Actions

Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.1	On hold / delayed	In progress	In progress		Live Love worked on the mapping of existing housing issues and challenges in buildings located in the blast impacted area. A full database has been compiled to breakdown the problems and possible solutions with involvement of different stakeholders. **UN Results Report 2021 3RF: Publication of a policy guide to inform a national housing policy/ strategy, titled "Mainstreaming Housing in Lebanon's National Urban Policy"**. **	1. Anti-Seismic structural retrofitting of heritage buildings to ensure resilience against future disasters. 2. Develop recovery plan around a cluster approach to upgrade the quality of open spaces in neighborhoods and potentially intervene on urban infrastructure (Street lighting, sanitary, electrical and mechanical networks etc.). 3. Promote participatory approach in coordination with residents to develop a holistic recovery plan.
	Develop a detailed housing recovery strategy and action plan, linking housing to wider urban recovery while remaining sensitive to heritage and the environment.	Coordination Planning Unit to be set up to develop recovery strategy.	EU-funded programmes to retrofit public buildings with green technology. Ensure that buildings are renewable energy ready, and install solar energy whenever possible.			
	Target date(s)	Before CG4	Continuous			
Responsibility		World Bank and UN Habitat	EU			
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.2	Achieved	Achieved	Achieved	Achieved	Live Love has fully rehabilitated over 450 Level 2 damaged units affected by the blast with budgets amounting to \$4000 to \$7000 per unit in the aim of Building Back Better. Live Love was awarded the Japan Funded project as implementing partner with UN-Habitat, Project for the rehabilitation of 11 heritage buildings and common open spaces. Collaboration made with Italian experts to upgrade structural integrity of the heritage buildings	•Rehabilitation of 100 apartments in Nabaa – Bourj Hammoud part of the Beirut Port Explosion efforts.
	Repair all minimally or partially damaged housing units of economically and socially vulnerable households	International efforts: Japan funded UN-Habitat Project- Rehabilitation of structurally damages residential buildings and public spaces on blast affected areas-, Canada funded IMC project- GAC 3871-, Australia funded Oxfam Project-Beirut Emergency Response and Netherlands funded Tabitha project- LIR-,	Live Love has fully rehabilitated over 450 Level 2 damaged units affected by the blast with budgets amounting to \$4000 to \$7000 per unit in the aim of Building Back Better. Live Love was awarded the Japan Funded project as implementing partner with UN-Habitat, Project for the rehabilitation of 11 heritage buildings and common open spaces. Collaboration made with Italian experts to upgrade structural integrity of the heritage buildings	Mapping of efforts by FER (Lebanese Army).		
	Target date(s)	Done	Done	Done		
Responsibility						Re-assess vulnerability criteria previously used given the rapid depreciation of the currency and economic situation in the country.

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.3	In progress	In progress	Achieved		LFF Beirut Housing project became operation 25 February.	
	Stabilize heritage housing.	LFF Beirut Housing Rehabilitation and Cultural Heritage and Creative Industries Recovery. Support the rehabilitation of residential buildings of heritage value and provide access to secure rental solutions for vulnerable households, and provide emergency support to creative entities and practitioners, affected by the Beirut Port explosion.  The 13M USD project is expected to be signed late July 2021 with UN-Habitat and implemented with the support of UNHCR and UNESCO starting from early August.	Live Love has worked with the Beirut Heritage Initiative to stabilize, cover, and protect over 20 Heritage Buildings in the blast affected area through a project funded by ALIPH Foundation. * LL has fully renovated four Heritage Buildings with 11 buildings in progress right now.			
	Target date(s)	Q1				
Responsibility		WB/UN Habitat	Live Love and BHI			
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.4	In progress	Achieved	In progress			
	Launch a rental subsidies program for the most vulnerable among the displaced.	Mapping of rental challenges and break down of case studies and possible solutions done by LL.	Planning Coordination Unit can develop template rental contracts to address both tenant and landlord rights.			
	Target date(s)	Done	Q2			
Responsibility		Live Love	PCU			

Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.5	In progress	In progress	In progress		In Progress: Discussions held with the Engineering department at the Beirut Municipality to work on strengthening and supporting the department and providing office spaces for them + Equipment.	Work on digitizing permit obtainance process with a tailor made smart tracking system for requests and applications
	Establish a city-wide, multi-stakeholder platform to develop a housing and urban recovery strategy; define organization and implementation measures.	Discussions held with within 3RF Housing WG to set up a Coordinaion Planning Unit inside the municipality. ToR is being drafted by WG.	Work on Smart Urban Design to ensure Green Spaces, access to disabled and other inclusion actions, sustainable urban farming, community waste recycling and reuse, etc. Solutions should also consider long-term livelihood and ensure that efforts create quality jobs. Therefore, actions should include strong element of capacity building.			
	Target date(s)	Before CG4	Continuous			
Responsibility		World Bank and UN Habitat	PCU			
Track 2 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.6	On hold / delayed	Not yet started				The solutions and processes proposed in the Japan project with UN-Habitat is an exercise that could be used as a reference or lessons learned for the advancement on that front.
	Adopt policy interventions to lower housing costs and incentivize investment in affordable housing solutions as part of reconstruction.					
	Target date(s)	Continuous				
Responsibility		PCU				
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments

4.1.7	In progress	In progress				
	Develop a national housing policy with an emphasis on affordable housing markets and urban regeneration; make it part of an integrated approach for neighborhood upgrading	Identify and build relationships with government counterparts. OEA President can set a meeting with the Mohafez to discuss this possibility. The housing sector is support through the projects that are part of a complex international institutional effort to support the recovery from the BPE. There are limited government programs in the urban construction sector.				
	Target date(s)	Q2				
Responsibility		PCU				
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.8	In progress	Achieved				
	Incentivize and assist with repairs and conservation of historic residential buildings by the end of 2021; support both owner-driven and community-led approaches for historic neighborhoods	Live Love has worked with over 20 different heritage cases in negotiation with building owners and local residents. LL was one of the first local organizations to adopt the cluster community-led approach in reconstruction.				
	Target date(s)	2021				
Responsibility		Live Love				
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.9	In progress	In progress				
	Reconstruct housing units for the most economically and socially vulnerable; provide strategic guidance, technical and financial support, and capacity building for tenants and homeowners.	Local CSO efforts. (Please provide description)				The solutions and processes proposed in the Japan project with UN-Habitat is an exercise that could be used as a reference or lessons learned for the advancement on that front.
	Target date(s)					
Responsibility						

Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.1.10	On hold / delayed					Empowerment and promotion of Local industries especially in construction materials, Ex. First locally made Lime Plaster and mortar was tested and used by Live Love in the Rmeil Cluster (Project in partnership with UN-Habitat)
	Establish a monitoring system for the housing supply chain (construction materials and price levels) and the rental market, including market indicators such as vacancies and individual evictions (targeting the poor, refugees, and migrant workers).	PCU to take up				
	Target date(s)	Q2				
Responsibility		PCU				

4.2 Port

Track 1 Commitments

Reforms / Policy Actions

Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.1	<b>In progress</b> Establish a vision and reform principles for the port sector, to inform the reconstruction strategy.				In terms of the reform aspect, the World Bank published a policy note in January 2021 titled "Reforming and Rebuilding Lebanon's Port Sector: Lessons from Global Best Practices" as well as a positioning paper titled "Governance Framework for the Port Sector of Lebanon" with the Port of Rotterdam and the group of experts. The papers were followed by a first webinar jointly organized with the Netherlands on February 12, 2021 to discuss the need for a port sector law and governance reforms and engage with local stakeholders. The World	
Target date(s)						
Responsibility						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.2	<b>In progress</b> Adopt a vision statement that lays out the principles for port sector reform and a reconstruction strategy, including for customs.					
Target date(s)						
Responsibility						
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.3	<b>In progress</b> Conduct detailed assessments of contamination at the explosion site and address immediate needs, including site clearance, silo dismantling, rubble removal, dredging, removal of damaged vessels, and safe management of waste (including grains and hazardous waste).					
Target date(s)						
Responsibility						
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.4	<b>Achieved</b> Facilitate general cargo processing at the Beirut container terminal, the Port of Tripoli, and/or the Port of Saida; set up temporary storage and warehousing solutions to ensure the continuity of supply chains and reduce food security risks.					
Target date(s)						
Responsibility						

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3		Additional notes / comments
4.2.5	In progress					
	Address the immediate needs of clearance processes and storage to restore capacity, resume inspections, and minimize delays and disruptions to supply chains.					
Target date(s)						
Responsibility						
Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.6	On hold / delayed					
	Establish clear institutional arrangements to manage hazardous materials and waste from construction and demolition.					
Target date(s)						
Responsibility						
Track 2 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.7	On hold / delayed				awaiting a new Government	
	<u>Enact a new port sector law addressing the port authority's operations as well as customs.</u> The law would define the respective roles of the government, the port authorities, and commercial operators, as well as their relationships in terms of duties, rights, and responsibilities. It would be based on the landlord port principles, opening up commercial operations and reconstruction to the private sector under a clear regulatory framework to safeguard the public interest and ensure full transparency in financial management and operations.				With regards to Lebanese Customs and border management processes, the World Bank and AFD are finalizing a paper on Port and Maritime Trade Digital Policies. AFD and the French Treasury have also financed experts to conduct a stakeholder mapping and diagnostic of existing procedures as a preliminary step before reengineering and computerization. Italian Customs have been providing technical assistance to Lebanese Customs and have provided 2 scanners to respond to their needs. UNODC is implementing its Container Control Program (CCP) to assist Customs and other law enforcement agencies in identifying, profiling and inspecting high-risk containers on Lebanese sea, air and land borders. The EU ICMPD IBM Project is delivering trade facilitation and customs procedures/processes/controls assistance to the Lebanese Customs Administration (LCA) through a joint LCA – ICMPD – UNODC Risk Management Working Group and a Trade Facilitation Working Group. The EU ICMPD IBM Project also started a project on the implementation of Standard Operating Procedures on customs	
Target date(s)						
Responsibility						



	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.8	On hold / delayed					
	<u>Develop a national strategy for economic corridors and ports/maritime clusters, revisiting the siting and sizing of the port; rebalance roles and investments in the Tripoli port and other logistics infrastructure such as dry ports and the rail network; use an economic corridor approach to better position Lebanon to play an important role as a regional hub for maritime transport.</u>					
	Target date(s) Responsibility					
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.9	On hold / delayed	In progress			PoB chose to amend Khatib & Alami's ongoing contract to modify the masterplan but has not taken any action in this regard yet. As for the masterplanning, and at the request of the Port of Beirut Management and Operating Committee, UN-ESCWA completed a study in December 2020 on the main guidelines for the adjustment and update of the 2018 master plan, and the final report was presented to PoB. A strategic study was also conducted by HPC/Roland Berger/Colliers early April 2021 on the development of the PoB and adjacent land (urban development).	
	Review the Port of Beirut master plan in light of guidelines and principles set in the national strategy to optimize the number, size, and location of facilities; address urban congestion around the port; enhance logistics efficiency and the handling of hazardous goods.	UN Results Report 2021 3RF: The draft TOR that the WB prepared for the detailed Study of the Master Plan of the Port of Beirut was peer-reviewed by UNESCWA (Milestone)				
	Target date(s) Responsibility					
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.10	On hold / delayed				subject to governance reforms, a vision and strategy for the port sector, as well as a revised masterplan.	
	Reconstruct the enabling infrastructure at the port and identify potential public-private partnerships (PPPs) to leverage private investment and support the recovery and reconstruction program. This would include redefining the principles for the container terminal concession, regularizing existing contracts, and preparing reconstruction contracts in line with the new port sector law, procurement reform, and the law on PPPs.					
	Target date(s) Responsibility					

Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.2.11	On hold / delayed				subject to the new port sector law.	
	Establish a new port authority and nominate a board in a transparent manner based on professional qualifications, with responsibilities and accountabilities clearly spelled out. Encourage women's involvement in leadership and management positions, including the board.					
	Target date(s) Responsibility					
4.2.12	In progress					
	Recognize and define the mandate and role of port communities in management of the sector and monitoring of its performance. In addition to the port authority, local port communities would have an official role under the new port sector law, to establish from the outset a clear pattern of trust among all port stakeholders. Both in Beirut and Tripoli, organize these communities by identifying local champions who have the trust of their peers and the clout to bring together all port stakeholders.					
	Target date(s) Responsibility					
4.2.13	On hold / delayed				training and secondment proposals offered but no response from PoB.	
	Build capacity at the ministerial and port levels through peer secondment and trainings to ensure that both levels are fully aware of the laws, decrees, decisions, and institutional and regulatory frameworks; that they have the expertise required to carry out their duties; and that women are encouraged and trained for leadership positions.					
	Target date(s) Responsibility					

**4.3 Electricity**

**Track 1 Commitments**

Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.1	On hold / delayed	Achieved	In progress		Policy document was approved by CoM on 25 February.	
	Establish a vision that lays out sector reform needs and actions.	Policy document with medium term needs to reach sustainable state. World Bank is supporting.	Short-term (2 years) action plan to reduce losses and increase generation of electricity. Will be discussed at 4 February Council of Ministers.			
	Target date(s)	Q1	Q1			
Responsibility		MoEW and World Bank	MoEW and World Bank			

Investments / Programs

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.2	Achieved	In progress				
	Complete measures on the distribution network to temporarily restore electricity service in the explosion area	Part of short term action plan (milestone 2 above).				
	Target date(s)	Q1				
Responsibility		MoEW and World Bank				

Institutional Strengthening

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.3	On hold / delayed	In progress				
	Prepare an action plan for restoring EDL's essential functions in line with the vision of the utility's future role as a transmission operator in Lebanon's electricity sector.	Covered by medium and short term plans above.				
	Target date(s)	Q1				
Responsibility		MoEW and World Bank				

**Track 2 Commitments**

Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.4	On hold / delayed	In progress				
	Recruit members of the Electricity Regulatory Authority and operationalize ERA.	Covered by medium and short term plans above.				
	Target date(s)	Q1				
Responsibility		MoEW and World Bank				

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.5	On hold / delayed	In progress	On hold / delayed	Achieved	Contract expired for all DSPs on 21-12-2021 and extended on the basis of Law 160 (extension of deadlines) to all DSPs for a period of near 18 months. All DSPs accepted the extension except the company operating lot 2 (Beirut and Bekaa) which considered the extension on the same contract terms to be not viable for the project. Other DSPs committed to a certain amount of reductions in losses conditional on required responsiveness of ministries and directorates in the Lebanese government.	<p>challenges in the distribution sector, such as; shortage of material, halting investment projects, delaying the roll out of smart meters, delaying DSPs payments.</p> <p>- EDL is facing internal pressure from employees who are against any change or reduction in their roles so that they do not become redundant. This will be a major obstacle against the establishment of private sector concessions.</p>
	Establish private sector concessions for the distribution network before expiration of the distribution service provider contracts.	Studies into this are part of short term action plan (milestone 2 above).	Tender process. (Unlikely soon, given current economic situation.)	Contracts with Distribution Service Providers were due to expire end 2021, but were extended with reference to COVID.		
Target date(s)		Q1	Unlikely soon	Done		
Responsibility		MoEW and World Bank	MoEW and World Bank			
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.6	On hold / delayed	Achieved			<p>The Lebanese Distributed Renewable Energy Generation Draft Law is planned to be discussed at the Council of Ministers but no date has been set yet.</p> <p>-The Law aims at enabling 'distributed renewable energy generation' (only) to benefit from various net metering arrangements, namely: (1) 'Single owner net metering', (2) 'Basic meter aggregation', (3) 'Tenant meter aggregation', (4) 'Multi-site aggregation', and; (5) 'Virtual' or 'community' net metering. The Law also aims at enabling 'distributed renewable energy generation (only) to benefit from direct (corporate) on-site and off-site power purchase agreements (PPAs), and renewable energy equipment leasing</p>	
	Revise building codes and facilitate concessional financing to incentivize energy efficiency and renewable energy upgrades (initially for reconstruction of damaged or destroyed buildings in Greater Beirut, then expanded to other parts of the country).	Law draft on renewable energy.				
Target date(s)		Done				
Responsibility						

Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.7	In progress	Achieved	In progress	In progress	<p>National Control Center (NCC): EBRD appointed a consultant (EDF) to initiate the assessment study for the establishment of an interim national control center. Work related to the NCC is split in two parts: the interim/"light" solution and the permanent solution.</p> <p>-For the interim solution, the assessment has been completed and the tender will be launched in the next few weeks. The interim location of the NCC will be either on the 8th floor (old location) or at the ED level.</p> <p>-Regarding the permanent solution, the detailed assessment is premature. Instead, EBRD probed EDL regarding the structural integrity and safety of the building for it be able to host the NCC long term. As a result, EDL prepared a building structural assessment tender and sent it to the Ministry of Energy and Water and the</p>	it is to be noted that all the discussed updates and processes are moving very slowly due to the government's lack of funding.
	Repair the Achrafieh electricity substation, clearing rubble and rebuilding EDL's administrative office, data center, and the National Control Center (along with its backup center).	Achrafieh electricity substation: EBRD appointed a consultant (EDF) who finalized the assessment for the damages of the substation and developed the tender documents related to the repair works according to the World Bank's procurement rules and regulations.	EBRD is currently trying to secure \$5 million from internal resources for implementing the rehabilitation works, but that approval of this funding is still not assured.			
	Target date(s)	Done	Stalled due to lack of fundin	Stalled due to lack of fundin		
Responsibility			EBRD	EBRD		
Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.8	On hold / delayed	In progress				
	Establish an interim public consultation mechanism to ensure public support for sector plans and the development and recovery of EDL pending the operationalization of ERA; include public consultation for regulatory rulemaking and approval of sector plans and investments.	Govt aware consultation on plans needed, but sensitive given potential tariff increases. 3RF WG could be springboard to public consultation.				
	Target date(s)	ASAP				
Responsibility		MoEW and World Bank				

4.3 Environment

Track 1 Commitments

Reforms / Policy Actions

Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.1	<b>In progress</b> Develop a strategy and action plan for greening reconstruction and urban design for the city of Beirut.	<b>Achieved</b> LFF "Beirut Critical Environment Recovery, Restoration and Waste Management Project" is prepared	<b>Not yet started</b> An engagement plan that identifies actions in greening the reconstruction agenda meeting gender-differentiated needs & interests is developed		Under the LFF / ENV Program (P176635), the Sub-Component 2.1 will support the development of strategic and sustainable activities aiming at greening the reconstruction agenda of Beirut city and Port of Beirut and which will be based on specific action plans to respond to priority issues covering (i) mitigation of Environment, Health and Safety risks; (ii) SWM action plan for Beirut city, (iii) integrating climate considerations in the reconstruction agenda, and (iv) engagement plans to adequately address barriers to participation of women and men and identify actions in greening the reconstruction agenda meeting gender-differentiated needs and interests. UNDP's post-blast area-based recovery efforts in Karantina included mainstreamed renewable energy measures.	
Target date(s)	Q4 2022	Q3 2021	Q3 2022			
Responsibility	MoE, UNDP, WB	UNDP, WB	UNDP, WB			
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.2	<b>In progress</b> Conduct detailed assessments of the waste streams outside the Port of Beirut, implementing priority waste management interventions (such as rubble), and rehabilitating damaged waste management infrastructure (e.g., sorting facility at Karantina, composting facility at Coral, health care waste facilities).	<b>Achieved</b> Assessments conducted for the collection and safe storage of more than 150,000 tons of mixed debris generated by the Beirut Port Explosion has been managed.	<b>In progress</b> Assessments for waste management in the Port of Beirut and dredging in Basin 4 are conducted.	<b>In progress</b> A plan for the environmental waste management of construction & demolition waste is developed under the LFF project	UN-Habitat has initiated needed testing and management plans for the management of the construction & demolition waste (CDW) temporarily stored at Bakalian site. Plans for the environmental waste management of CDW outside the Port will be developed under the LFF / ENV Program (P176635), the Sub-Component 1.2 & 1.3 Building on the Assessment and Plan for Waste Management in the PoB which was conducted by the EU immediately after the explosion, France has financed an in-depth assessment of waste and a plan through Recygroup. In-depth due diligence of the activities in Bakalian site have been conducted. Alternatives for asbestos contaminates rubble is being identified. Dutch government has developed ToRs for the assessments needed for dredging of Basin 4, including needed environmental assessments. Initial sorting of the CDW had been completed.	
Target date(s)	Q4 2022	Q3 2021	Q2 2022	Q4 2022		
Responsibility	UNDP, WB, UN Habitat, France, Netherlands	UNDP, WB, UN Habitat	France, Netherland	UNDP		
Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.3	<b>In progress</b> Establish a collaborative platform for stakeholder engagement in greening the reconstruction agenda; a pilot activity will also be developed to respond to ISWM needs in the affected areas by the explosion	<b>In progress</b> A collaborative platform is established in consultation with NGOs	<b>In progress</b> A pilot activity that responds to ISWM needs in the areas affected by the Beirut Port Explosion is identified	<b>Not yet started</b> The pilot activity identified under Milestone 2 is implemented	Under the LFF / ENV Program (P176635), the Component 2 will support a collaborative platform for stakeholders' engagement and implementing priority actions for greening Beirut's reconstruction agenda. Continuous consultations with NGOs are underway for establishing the collaborative platform and identification of activities to be implemented under the pilot ISWM project	
Target date(s)	Q4 2022	Q2 2022	Q2 2022	Q4 2022?		
Responsibility	UNDP, WB, EU, CSOs	UNDP, WB, EU, CSOs	UNDP, WB, EU, CSOs	UNDP, WB, EU		

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.4	In progress	Achieved			Under the LFF / ENV Program (P176635), the Component 2 will support environmental monitoring and enforcement activities for critical hazardous materials, whereas its Component 1 will be securing the explosion site at the port by implementing necessary site containment and management measures to address risks from waste. Monitoring protocols for project design and project env & social safeguards requirements have been designed. These will provide a basis for developing an environmental baseline	
	Strengthen environmental monitoring and enforcement of environmental, health and safety measures in Beirut, including the port.	Monitoring protocols for project design and project environment & social safeguards requirements have been designed				
Target date(s)		Q1 2021 (Feb)				
Responsibility		UNDP, WB				
Track 2 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.5	In progress	In progress			Several on-going initiatives are identifying priority legal framework to be developed. Initiatives include the following: EU/TADWEER project; WB/UPOPs project; Expertise France is also supporting Ministry of industry in this field	
	Develop the legal framework for storage and handling of chemicals	Priority legal framework(s) to be developed have been identified				
Target date(s)		Q2 2022 (Jun)				
Responsibility		WB, Expertise France, EU, UNDP				
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.6	In progress	In progress			Various initiatives funded by UNDP and WB will support priority regulatory framework for ISWM. Identification and support for needed regulations is underway through various on-going initiatives	
	Identify complete needed regulations/ standards related to the Integrated Solid Waste Management (ISWM) Law	Regulations that are needed for ISWM and the support they require are identified				
Target date(s)	Q4 2023	Q4 2023				
Responsibility	UNDP, WB	UNDP, WB				
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.7	In progress	Achieved	In progress		The Strategic Environmental and Social Assessment of the draft ISWM strategy was initiated under the WB Lake Qaraoun Pollution Prevention Project and will allow technical review and consultative process to support the adoption of the strategy. The 1st deliverable is the scoping report and the 2nd is the SESA report. Continuous consultations will be planned in view of finalizing the ISWM strategy	
	Adopt the national ISWM Strategy and develop a participatory solid waste management plan for Beirut.	The Strategic Environmental and Social Assessment of the draft ISWM Strategy is launched	The scoping report and Strategic Environmental and Social Assessment report are published			
Target date(s)	Q4 2022	Q3 2021 (Oct)	Q1 2022 (Mar)			
Responsibility	MoE	MoE, CDR, WB	MoE, CDR, WB			
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.8	In progress	Achieved	In progress		With GoL funding and Combilift, Combilift safely packaged containers at the PoB containing hazardous material and shipped these to Germany for treatment With funding from France, Recygroup has signed a contract with Ministry of Economy for the management of grains in the silos Recygroup signed a contract with PoB to develop management plans for the clean up of the waste generated by the explosion in PoB	
	Implement management plans for various waste streams (including hazardous material, electronic waste, and scrapped vehicles) and for restoring affected natural ecosystems (marine and green cover).	59 containers of hazardous waste have been safely packed and removed from the Port of Beirut	The management of the clean up of grains in the silos is implemented			
Target date(s)	2023	Q3 2021	Q2 2022			
Responsibility		GoL, Combilift	France, Recygroup			

Institutional Strengthening						
	BRF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.9	In progress	Achieved	In progress		Initiation of a project by Expertise France to qualitatively assess industries using hazardous chemicals in their facilities and those being stored in public facilities, to assess their current storage conditions and raise recommendations for the industries to properly store their hazardous chemicals. The government (through PMO) collected data and information from public facilities related to hazardous chemicals stored. Training activities for Ministry of Industry are currently underway	
	Conduct an inventory and audit of chemical stockpiles and hazardous materials in Beirut.	Contract with Expertise France for qualitative assessment of industries using hazardous materials is signed.	Industries using hazardous chemicals in their facilities and chemicals being stored in public facilities are qualitatively assessed and recommendations for proper storage are made			
	Target date(s)	Q4 2022	Q4 2021	Q3 2022		
Responsibility	Expertise France, PMO	Expertise France, PMO	Expertise France, PMO			



4.3 Municipal Services

Track 1 Commitments

Reforms / Policy Actions

Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.1	In progress	In progress	Not yet started	Not yet started	The recommendations under Milestone 3 will feed into coordination with the Housing Working Group on the LFF Housing and CCIs project that envisions the establishment of a "Planning and Coordination Unit" (PCU) in Beirut. Consultations and discussions with municipal concerned entities have already started	
	Develop a framework that consolidates the process for obtaining repair, rehabilitation, and reconstruction permits and is coherent with the housing recovery action plan and strategy.	A roundtable with municipalities on the current process of obtaining permits has taken place, providing an understanding of the baseline for the development of the permits framework	A knowledge exchange between (WB) experts working on other countries' permit frameworks and Greater Beirut's municipalities has taken place	A set of recommendations for developing the permits framework is finalized and shared with the municipalities based on the roundtable and knowledge exchange		
	Target date(s) Responsibility	End of 2022 UN-Habitat, World Bank	early Q2 2022 WB, UN-Habitat, NGOs, CSOs, M	late Q2 2022 WB, UN-Habitat		
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.2	In progress	In progress	In progress	Not yet started	Milestone 1: A public space in Karantina was rehabilitated and completed; remaining five in progress. Additionally, HIV/TB center and MoPH warehouse that was severely damaged by the blast have been rehabilitated and equipped with medical equipment. Milestone 2: An integrated digital data system (e-governance) in Beirut municipality is being developed. Engineering dept. at the municipality of Beirut has been capacitated to digitize data (using Geographic Information System - GIS) of municipal assets; Milestone 3: UNOPS hired a consultant to map all municipal infrastructure in the blast affected areas and survey selected key infrastructure and assets based on a set of technical and social considerations. The consultant started consultations with Beirut and Bourj Hammoud municipalities. A follow-on milestone will be that the selected and surveyed key infrastructure is	
	Rehabilitate damaged roads and mobility infrastructure, storm water drainage, public spaces, buildings owned by municipalities, and social housing.	Six public spaces in Karantina & Mar Mikhail are rehabilitated, increasing accessibility and promoting safe and secure urban spaces for all, including children	The Beirut and Bourj Hammoud municipalities have participated in a series of capacity building measures on digitizing data, and the operation and maintenance of rehabilitated infrastructure	A mapping of all municipal infrastructure in the blast-affected area and a survey of selected key infrastructure and assets is completed		
	Target date(s) Responsibility	End of 2024 UN-Habitat, UNICEF, UNOPS	Q2 2022 UN Habitat, UNICEF	Q3 2022 UNOPS, UN Habitat		

Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.3	In progress Establish a one-stop shop in the Beirut and Bourj Hammoud municipalities for the following key functions: to obtain repair, rehabilitation, and reconstruction permits for damaged municipal services, residential and commercial properties, and cultural heritage building, among other facilities; to coordinate and share responsibilities among service providers, line ministries, and municipalities; and to communicate and disclose information, budgets, and expenditure for citizens.	Achieved Municipal social cell and drop-in center is established, to coordinate with stakeholders, including vulnerable communities. A regional technical office is established in Bourj Hammoud Municipality.	In progress Study of the Independent Municipal Fund (IMF) is completed	In progress A Planning and Coordination (PCU) is established	Milestone 1: - Regional Technical Office (RTO) was established under the municipality of Bourj Hammoud. - Municipal Social Cell was established under the municipality of Beirut to map and assess challenges related to migrants and propose mitigation measures through interventions. Milestone 3: The Housing and Municipal Services Working Groups have drafted the ToR of the PCU, it is being reviewed by/with the Mayor and Governor. This commitment (4.3.3.) is closely coordinated with the Housing and Culture Working Group and with the LFF Housing and CCLs project that consists of developing an 'Urban Recovery Strategy' and envisions the establishment of a "Planning & Coordination Unit" (PCU/one-stop shop) in Beirut.	Beirut municipality has increased capacity to accelerate Covid-19 pandemic response and vaccination through the provision of mobile health clinic and IPC (Infection and Prevention Control) kits (UN Habitat & UNICEF)
Target date(s)	End of 2023	Q4 2021	Q4 2022	Q4 2022		
Responsibility	UN-Habitat, UNICEF, WB	UN-Habitat	WB	WB, UN-Habitat, NGOs, CSOs, Governor		
Track 2 Commitments						
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.4	In progress Upgrade the industrial and commercial area in Bourj Hammoud, with urban regeneration and upgrading of affected and vulnerable neighborhoods.	In progress A Child-Friendly City Roadmap is developed and used to inform the urban regeneration of affected neighbourhoods	Not yet started Five priority measures to upgrade and regenerate the industrial and commercial area of Bourj Hammoud are identified through the WG's consultations & community participation with the Bourj Hammoud municipality	Not yet started Four priority measures identified under Milestone 2 are implemented	This commitment concerns Bourj Hammoud mainly & targets the enhancement of participation in decision making and project selection. Milestone 2: Under the LFF 'Beirut Housing Rehabilitation and Culture and Creative Industries Recovery' project, cultural productions (entities and individuals) will be supported to revive their businesses (see Culture WG's milestones). Milestone 3: UN-Habitat is currently discussing the strategic plan of Bourj Hammoud with 4 main identified priorities. Target date might change	
Target date(s)	Q3 2023?	Q3 2022?	Q3 2022?	Q4 2023		
Responsibility	UN Habitat, WB, CSOs, Bourj Hammoud Municipality	UN Habitat, UNICEF	UN Habitat, CSOs, Municipality	UN Habitat, WB, CSOs		
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.3.5	Not yet started Establish public consultation mechanisms for reconstruction plans to ensure that citizens' needs are integrated into these plans; include traditional channels, municipal website, and one-stop shop as well as social media.	Not yet started Two public (in-person) consultations on citizens' reconstruction needs have taken place - one in Beirut and one in Bourj Hammoud - to reach those who lack access to online consultation formats	Not yet started A 'virtual townhall' consultation on citizens' reconstruction needs has been conducted using the 3RF online citizen engagement platform or the municipal website	Not yet started Two-three communication channels have been used to inform the public about how their reported needs have been taken into consideration in the reconstruction plans	This commitment (4.3.5) is linked to the Housing Working Group's commitment to establish a city-wide, multi-stakeholder platform to develop a housing and urban recovery strategy and shall be coordinated accordingly	
Target date(s)	End 2022	Q2 2022	Q3 2022	Q4 2022		
Responsibility	UN Habitat, WB, Municipalities, CSOs	UN Habitat, Municipalities, CSOs	UN Habitat, Municipalities, CSOs	WB, UN Habitat		

4.4 Education

Track 1 Commitments

Reforms / Policy Actions

Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.1	In progress				<ul style="list-style-type: none"> <li>- MEHE is finalizing the National Remote Learning Plan (covering two academic years 2021 and 2022), which supports and guides the continuation of learning during the COVID-19 pandemic, while adhering to the international and national guidance prevention measures. The plan sets out different scenarios that would be adopted by MEHE depending on the state of the pandemic (physical learning; blended learning; distance learning) and elaborates the main components of the remote learning plans including 1) Devices for learners; 2) Infrastructure and school equipment; 3) Educational content and learning management system; 4) Teacher readiness; and 5) Support to and from parents. The draft plan was shared with donors relevant UN agencies in March 2021 and is currently being reviewed by MEHE based on the compiled inputs.</li> <li>- School reopening in hybrid teaching mode relaunched in April 21 for Grade 12, May 5 for Grade 9 and pre-primary, and May 17th for all remaining grades.</li> <li>- Health reopening protocol "Health guide for educational institutions on preventive measures to prevent the transmission and spread of the SARS-CoV-2 virus that causes Covid-19 infection" has been finalized before the Beirut blasts and reported under the COVID response.</li> <li>- The protocol for reopening Non-Formal Education centers is also finalized and being translated to Arabic reported under the COVID response.</li> <li>- Psycho-social support interventions for the most vulnerable are reported under the LCRP and COVID Response.</li> </ul>	*Development of the MEHE Inclusive Back to Learning Initiative for information, advice and guidance for school directors and teachers. Consultation and Development of a MEHE/CERD National Learning Recovery Initiative (focus on Foundational Literacy, Numeracy, Psychosocial Support and accelerated curricula coverage) (UN).*
	Implement the policy for remote/hybrid learning and localization of back-to-school plans to ensure that quality learning is delivered and that, when possible, schools are safe to reopen; integrate psychosocial well-being into formal and non-formal education programs.					
Responsibility						
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.2	In progress				<ul style="list-style-type: none"> <li>- Commitment to provide 60,000 devices/ tablets for students and 1,050 devices for teachers (to deliver online classes) to support distance learning.</li> <li>On hold/Delayed</li> <li>-Capacity building program for teachers and trainers on distance learning will be delivered to MEHE and CRDP by technical partners.</li> </ul>	*Development and operationalization of the MEHE/CERD Pilot Summer School Programme (UN)*
	Provide multiple learning pathways, including hybrid and/or remote learning using both high and low technology, with a focus on the most vulnerable children and youth during school closure.					
Target date(s)						
Responsibility						

Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.3	In progress				<ul style="list-style-type: none"> <li>- Consultations on the National Remote Learning Action Plan were limited to sharing the draft plan with key UN and donor agencies for comments and inputs.</li> <li>- Consultation on the Five-Year Sector plan is underway. The draft plan was shared in March for feedback from key UN and donor agencies. Plan for wider consultations (with CSOs, unions, etc.) is yet to be developed and agreed upon.</li> <li>- Consultation and coordination on the rehabilitation of education institutes is taking place regularly with all partners and stakeholders including relevant ministries (Education and Culture), international partners, parliamentary committees, CSOs, and the private sector.</li> </ul>	
	Ensuring close consultation on education reform and the recovery and reconstruction agenda with key stakeholders, including relevant ministries, international partners, parliamentary committees, CSOs, the private sector, teachers' unions, and communities.					
Target date(s)						
Responsibility						
Track 2 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.4	On hold / delayed				<ul style="list-style-type: none"> <li>-MEHE is currently working on Lebanon's Education Five-Year Sector 2021-2025 with support from technical partners. The Five Year Plan is the first of two plans that will contribute to Lebanon's 2030 Strategy to achieve SDG 4, 'Quality Education for All'. It presents MEHE's comprehensive vision for the education sector post-RACE (National Strategy reaching all Children with education) with the identification of a set of 6 priorities. It includes TVET and Higher Education and General Education (ECE to Grade 12). A preliminary draft covering the general education sector was shared in March for feedback from key UN and donor agencies. Plan for wider consultations (with CSOs, unions, etc.) is yet to be developed and agreed upon. Higher education will be developed next with TVET to follow at an appropriate time. MEHE is currently working on the elaboration and review of the plan with technical support from different partners. The plan is aimed to be finalized at the end of June 2021.</li> <li>-The 5YP is the Overarching Framework to incorporate the spectrum of education related initiatives which can range from Emergency Access Back to School as part of the Lebanon Crisis Response Plan (LCRP), to targeted programs like the Multi-Year Resilience Plan, and Bilateral Programmes with Donors and Direct Funding activities with Partner Governments, and National and International Non-Governmental Agencies.</li> <li>-Catch up/Accelerated learning programs (which include the development of assessment tools, materials, teacher training and delivery (pilots) and initiatives targeting drop outs and support to higher education sector strategy have been implemented.</li> <li>- Implementing communication strategies to support school enrollment and retention, including establishment of a referral mechanism.</li> </ul>	*Development of the MEHE General Education 5 Year Plan, Single MEHE Annual Work Plan and Draft MEHE Coordination Structure to support delivery of results (Note: Includes approval of MEHE Education Cannot Wait Multi-Year Resilience Programme aligned to the 5 Year Plan) (UN).*
	Prepare a new 5-year Strategic Education Sector Plan using recent evidence and engage in broad public consultations. The plan should focus on immediate, medium, and long-term needs for better learning at all levels, including early childhood education, building on the school quality assurance framework.					
Target date(s)						
Responsibility						

Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
	In progress					
4.4.5	Begin immediate rehabilitation and reconstruction, including refurbishing of damaged furniture and equipment, based on the final technical assessments of damage to education facilities.				<p>Rapid and technical assessments by MEHE and partners related to the impact of the Beirut port explosions on education institutions and the rehabilitation needs have been finalized and circulated. Based on these assessments, the Beirut blasts caused damages in:</p> <ul style="list-style-type: none"> <li>•94 public schools</li> <li>•At least 132 private schools reported damages</li> <li>•20 TVET buildings</li> <li>•32 universities, including the Lebanese University</li> </ul> <p>Progress of rehab works in schools is as below and it ranges between minor and major reconstruction work depending on the level of damages (light, moderate, severe) identified in the assessments:</p> <ul style="list-style-type: none"> <li>•19 public schools handed over to MEHE</li> <li>•55 public schools completed and in the process of handover to MEHE</li> <li>•20 public schools, including 5 severely damaged, are ongoing.</li> <li>•58 private schools carried out/ completed their own works and 74 are being rehabilitated by different partners (32 completed; 22 unreported; the rest ongoing)</li> <li>• Provision of equipment and furniture for damaged public schools is currently in the procurement phase for all schools (except for 3 schools who already received their items). Distribution of items to schools will be launched in June.</li> <li>•Rehabilitation of education institutions is being supported by different partners:</li> <li>•Swiss Agency for Development and Cooperation (SDC): 19 public schools)</li> <li>•UNESCO: 71 public and 20 private schools, 20 TVET buildings and 3 public and private universities</li> <li>•UNICEF: 4 public schools and 9 private</li> <li>•Other partners include the French Government (22 private schools) and other NGOs and private foundations for the rehab of private schools</li> </ul>	*Completion and handover of all planned rehabilitation work (94 public schools, 132 private schools, 20 TVET buildings and 20 Lebanese University buildings, and 2 private Universities) (UN)*
Target date(s)						
Responsibility						

4.4 Health

Track 1 Commitments

Reforms / Policy Actions

	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.1	<b>In progress</b> Align the mechanism to identify the most vulnerable with those used by other sectors (e.g., social protection); expand it as needed to reach the vulnerable with subsidized essential health services.					
Target date(s)						
Responsibility						

Investments / Programs

	3RF Commitments	Milestone 1: identification of sites	Milestone 2: development of IRM model	Milestone 3: full implementation of IRM model	Description of status	Additional notes / comments
4.4.2	<b>In progress</b> Support implementation of a subsidized package of primary health care services through a network of 21 Primary Health Care Centers (PHCCs) in the explosion-affected area in line with the Ministry of Public Health's Immediate Response Model.				In total IMC supported 6 PHCCs out of 21 PHCCs affected by Beirut Blast. Using EU MADAD funding IMC have been supporting 4 out of the 21 PHCCs with the REBAHS Model prior to the blast and continued to do so afterwards. Complementary activities using OCHA and private funds occurred at these 4 PHCCs. IMC has added 2 PHCCs (Horj and Msaytbeh: both Makassed PHCCs) under Private funding and not EU MADAD.  Moreover, PUI supported 4 clinics out of 21 PHCCs affected by Beirut blast. Two out of the four supported clinics are currently operating under the EU fund; while the complementary activities, at Hariri PHCC –Beirut and Khatam Anbiaa, are still being implemented under REBAHS 2 grant / REBAHS LPSP. The other two supported clinics, Bolgordgian and Zarif PHCCs, were handed over to Amel association between the second and the third quarters of 2021 as part of the consortium under AFD fund( SAQIRH).	*26,907 beneficiaries received subsidized PHC services in three PHCCs, and 6,300 mental health consultations delivered in 3 PHCCs and 1 specialized center; 15,000 women reached with SRH medical services and midwifery care including RH drugs and contraceptives and at least 18000 with information on SRH; Communication and outreach activities initiated in the affected PHCC catchment areas, focusing on PHCC promotion, Covid19 precautions, Immunization, IYCF and nutrition, reaching 110,000 caregivers (UN)*
Target date(s)						
Responsibility						

Institutional Strengthening						
	3RF Commitments	Milestone 1: stakeholders identified	Milestone 2: coordination with existing Health sector structures	Milestone 3: creation of the 3RF WG	Description of status	Additional notes / comments
4.4.3	<b>In progress</b> Establish a 3RF multi-stakeholder health coordination platform with balanced representation of civil society and other relevant stakeholders to ensure the transparency, effectiveness, and efficiency of the health response; reinforce the referral system, through stronger intra-ministerial cooperation and coordination; convene regular (e.g., biannual) multi-stakeholder health forums.	<b>Achieved</b>	<b>In progress</b>	<b>In progress</b>	The EU, WB and UN have been coordinating in order to streamline 3RF working group structure within existing health sector coordinating mechanisms that already exist in Lebanon - identification of the specific 3RF commitments and milestones has been done. The effective running of 3RF WG discussion will begin in Q4 2021. CSOs to be contacted and included in the mechanism for coordination.	
Target date(s)		Sep/21	Sep/21	Dec/21		
Responsibility		EU, WB, UN	EU, WB, UN	EU, WB, UN		
Track 2 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1: supporting hospitalisation services	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.4	<b>In progress</b> Develop a phased universal health coverage strategy to progressively expand beyond primary health care access for the most vulnerable in the blast-affected areas; ensure coverage of (i) additional services at secondary and tertiary levels of care and (ii) people in the rest of the country.	Support to hospitalisation			The WB is in final discussions with the GoL in order to finance the subsidisation of hospital bills for Lebanese patients as covered by MoPH.	
Target date(s)		Continuous				
Responsibility		WHO, GoL				

	3RF Commitments	Milestone 1:	Milestone 2:	Milestone 3:	Description of status	Additional notes / comments
4.4.5	In progress	In progress	Achieved	In progress	<p>In terms of the wider COVID response, vaccination procurement continues to be prioritised by MoPH and the international community. As at 2 November, GoL has secured around ~8M doses of COVID19 vaccines of which 4,587,550 have been delivered and 3,330,487 have been administered. ...). WB support has allowed for the procurement of 3,251,430 of these doses. The international community (DK, US, EU, DE, WB) is continuing to support COVID19 vaccines through providing funding for the procurement of vaccines and medical supplies needed for the administering of vaccines. The support will continue into 2022. The UN is supporting in the procurement of vaccines and medical supplies as well as the delivery of vaccines to Lebanon.</p> <p>In addition to the vaccination support, the international community is also supporting IPC, PPE and community awareness raising through projects in order to mobilise communities on the importance of measures for the prevention of COVID19 as well as COVID19 vaccinations. DE, WB and WHO are also in discussions with MoPH for a subsidisation scheme to support hospitals and health facilities supporting the roll out of COVID19 vaccines.</p>	<p>*8 public hospitals twinned with eight university hospitals for exchanging knowledge and bedside coaching on COVID-19 clinical management; Epidemiologic surveillance unit at MOPH supported with COVID diagnostics and genomic testing and with 64 additional staff for surveillance unit, call center, and contact tracing (UN)*</p>
Update the COVID-19 response strategy to include revised mitigation measures, including reimbursement schemes for hospitals and development of COVID-19 vaccination deployment and operational plan.	<p><b>COVID-19 response strategy updated :</b> The World Bank Lebanon Health Resilience Project is supporting MoPH in covering the cost of treatment for patients diagnosed with COVID-19 in public and private hospitals.</p>	<p><b>National Deployment and Vaccination plan finalized :</b> The NDVP was finalized in February 2021. The document is currently undergoing an update.</p>	<p><b>continuous adaptation and support for COVID19 response</b></p>			
Target date(s)	Continuous	Feb/21	Continuous			
Responsibility	MoPH and WB	MoPH	All			
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.6	In progress	Achieved	In progress	In progress	<p>Various donors have supported the reconstruction of Karantina hospital in Beirut which was heavily damaged by the Beirut Blast. Through the WHO the EU is supporting the procurement of medical supplies for the reconstructed Qarantina hospital. Primary health care centers damaged by the Blast have also been supported for the replacement of parts and specific doors / windows that have been damaged.</p>	<p>*Reconstruction and refurbishment of Central Drug Warehouse severely damaged by August Beirut Port explosions and physical rehabilitation of Central Supply Warehouse (including a dry room); Rehabilitation and reconstruction of Karantina governmental hospital and 3 PHCCs and provision of medical equipment and supplies to Karantina governmental hospital and MOSA SDCs; As part of the National Energy Strategy for the Healthcare Sector, conducted an assessment of hospital medical equipment to identify their energy needs and develop recommendations by hospital department for energy saving (UN)*</p>
Reconstruct heavily damaged facilities (with priority to those in the public sector) in line with green energy solutions and ensuring accessibility and inclusion for people living with disability.	identification of damaged facilities	initiation of works on damaged facilities	finalisation of works			
Target date(s)						
Responsibility						



	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.7	In progress					
	Develop mechanisms for retaining health personnel and for procuring essential medicines and medical supplies					
	Target date(s)					
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.8	In progress					
	Strengthen supply chain management.					
	Target date(s)					
Responsibility						
	3RF Commitments	Milestone 1: development of subsidised model	Milestone 2: roll out of support to PHCCs for the implementation of the subsidisation model	Milestone 3: full MoPH PHCC network implementation LPSP	Description of status	Additional notes / comments
4.4.9	In progress	Achieved	In progress	In progress	AS OF NOV 1st, IMC started implementing the LPSP at 47 ED/MDAD supported PHCCs. The uptake of the new top off packages has been slower than expected; especially, when preventive services are not viewed as priority for the population, given the recent economic crisis and the exponential increase in transportation costs (more than 10-15 times the original price before fuel subsidies were lifted). In parallel, PUI has 25 PHCCs under REBAHS 2 and 3 PHCCs under REBAHS LPSP. IMC/PUI continue to raise awareness on the importance of preventive services through community outreach activities and is closely monitoring the progress made.	*Treatment and diagnostic services for TB patients and PLHIV maintained despite the central units destruction, via decentralization, outreach and joint testing platform (TB, COVID, HIV). (UN)*
	Support implementation of a subsidized package of primary health care services through a network of PHCCs at the national level.	MoPH PHC department successfully developed the LPSP model	The model is currently being rolled out in the PHCCs within the network of MoPH with donor support for subsidisation			
	Target date(s)	Jun/21	Nov/21			
Responsibility	MoPH PHC department	MoPH, iNGOs, donors				

4.4 Water

Track 1 Commitments

Reforms / Policy Actions

Track 1 Commitments						
Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.1	On hold / delayed	On hold / delayed	Achieved			
	Ratify the updated National Water Sector Strategy.	Approval of National Water Sector Strategy by ....	A complementary short term (5yrs) Plan for the sector to deal with the financial crisis is drafted, discussed with the Donors and approved by MoEW and GoL			
	Target date(s)	30/03/2022	30/03/2022			
Responsibility		MoEW	MoEW - TA EU-AFD			
Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.2	In progress	In progress	In progress	In progress	The milestones indicated are not sequential	
	Provide technical assistance to the water utility most impacted by the blast, the Beirut Mount Lebanon Water Establishment (BMLWE), especially on operations and maintenance costs of the main infrastructure.	TA EU-AFD – reinforcement of Water Establishment technical capacities	EU MADAD project implemented by UNICEF – support on O&M Water Establishment	The emergency plan for dealing with the financial crisis is discussed with the Donors and responsibility for funding are shared between GoL, Donors and payers of the service		
	Target date(s)	until Dec 2025	until dec 23	30/03/2022		
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.3	In progress	In progress	In progress	In progress	Various coordination meetings held on a quarterly basis. Expected the formalization of a quarterly coordination group under the umbrella of the MoEW (supported by the TA EU-AFD) to follow-up on the reform process and follow-up also on implementation of 3RF plan. The table will put together MoEW, WEs, CDR (from Government side), International Donors and Civil society representatives.	
	Establish the Water Executive Committee to pilot transparent implementation of the updated water sector strategy and strengthen the role of municipalities within its framework.	approval TOR coordination	Coordination mechanism in place	Outcomes of the coordination mechanism shared with civil society		
	Target date(s)	15/03/2022	15/03/2022	30/03/2022		
Responsibility		MoEW - TA EU-AFD	MoEW - TA EU-AFD	Representative of civil society in Coord table		
Track 2 Commitments						

Reforms / Policy Actions						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.4	In progress	Achieved	In progress	Not yet started		
	Ratify the revised Water Code, which was approved in 2018, and its related decrees;	Ratify revised water code, done in December 2020.	Decrees prepared & feedback collected from civil society	Decrees are approved by GoL		
	Target date(s)		Aug/22	Dec/22		
Responsibility		GoL	TA EU-AFD & Representative of civil society	GoL		
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.5	In progress	In progress	Not yet started	On hold / delayed		
	Restructure the water tariff.	study about revision of tariff to be launched	Tariff study to get feedback from civil society	Ensure that volumetric tariff can be implemented nation-wide where water meters are present		
	Target date(s)	15/02/2022	28/02/2022	31/12/2022		
Responsibility		TA EU-AFD	Representative of civil society in Coord table	WEs + TA EU-AFD		
Investments / Programs						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.6	Achieved				An initial assessment was completed by UNICEF in the weeks after the Blast. Follow-up with BMLWE in the months after do not show additional damages not previously registered.	
	Undertake in-depth damage assessments of water and wastewater assets.					
	Target date(s)					
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.7	In progress	In progress	Achieved	In progress	Funds mobilized for rehabilitation of part of the key infrastructures considered as a priority for Beirut supply during first assessment and in collaboration with BMLWE (EU MADAD and Japan project implemented by UNICEF)	*Using French thematic funds, LCO demolished and reconstructed the ferric chloride water treatment facility in Dbaye and using Japanese funds, LCO upgraded damaged wastewater conveyors (UN)*
	Rehabilitate and strengthen damaged facilities, applying modern standards for operation and climate proofing considerations.	Funding list of projects identified	list of projects that can be considered as contributing to the 3RF (beyond Beirut Blast) is compiled and total amount of funds calculated	Implementation list of projects identified		
	Target date(s)	30/03/2022	30/03/2022			
Responsibility		UNICEF	UNICEF			

Institutional Strengthening						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.8	On hold / delayed	In progress			A campaign for subscription been launched in May 2021 (EU MADAD project implemented by UNICEF) No progress yet on the customer database.	*Upgrade the customer database at BMLWE and incentivize households to register their connections officially. This included a national public campaign to encourage the public to subscribe and pay their water bills, funded by EU-Madad. (UN)*
	Upgrade the customer database at BMLWE and incentivize households to register their connections officially.	the activity should be revised in line with the revised priorities of the sector and emergency plan				
	Target date(s)					
Responsibility						
	3RF Commitments	Milestone 1	Milestone 2	Milestone 3	Description of status	Additional notes / comments
4.4.9	In progress	Achieved			UNICEF has started a program for reinforcing communication department of BMLWE. A campaign for promoting branding of BMLWE and subscription (see point above) has been launched in May for BMLWE together with all the other Water Establishments (EU MADAD project implemented by UNICEF)	*Development of COVID 19 ecosystem developed by UNICEF in coordination with the 4 water establishments that includes, awareness signage system, awareness materials for public and staff, and provide IPC and PPE materials for the use of water establishments staff (UN)*
	Rebuild customer-centric communication and dialogue between the BMLWE and civil society organizations.	Civil society inclusion on 3RF working group and national water sector coordination.				
	Target date(s)					
Responsibility						
